



PT. PENAMAS
BOILER FIRE TUBE F-80 L

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			




Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

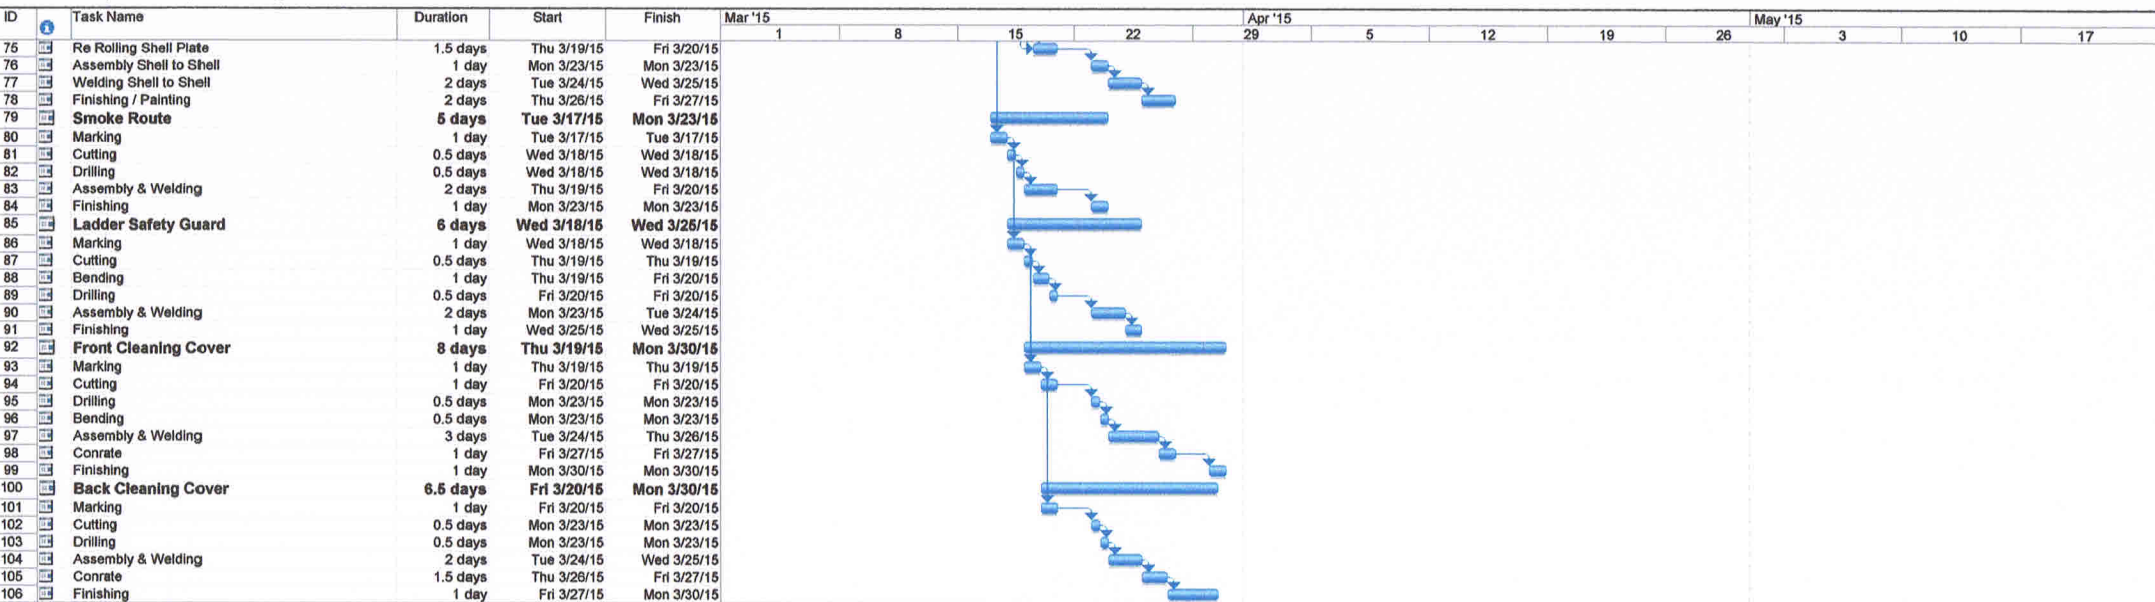

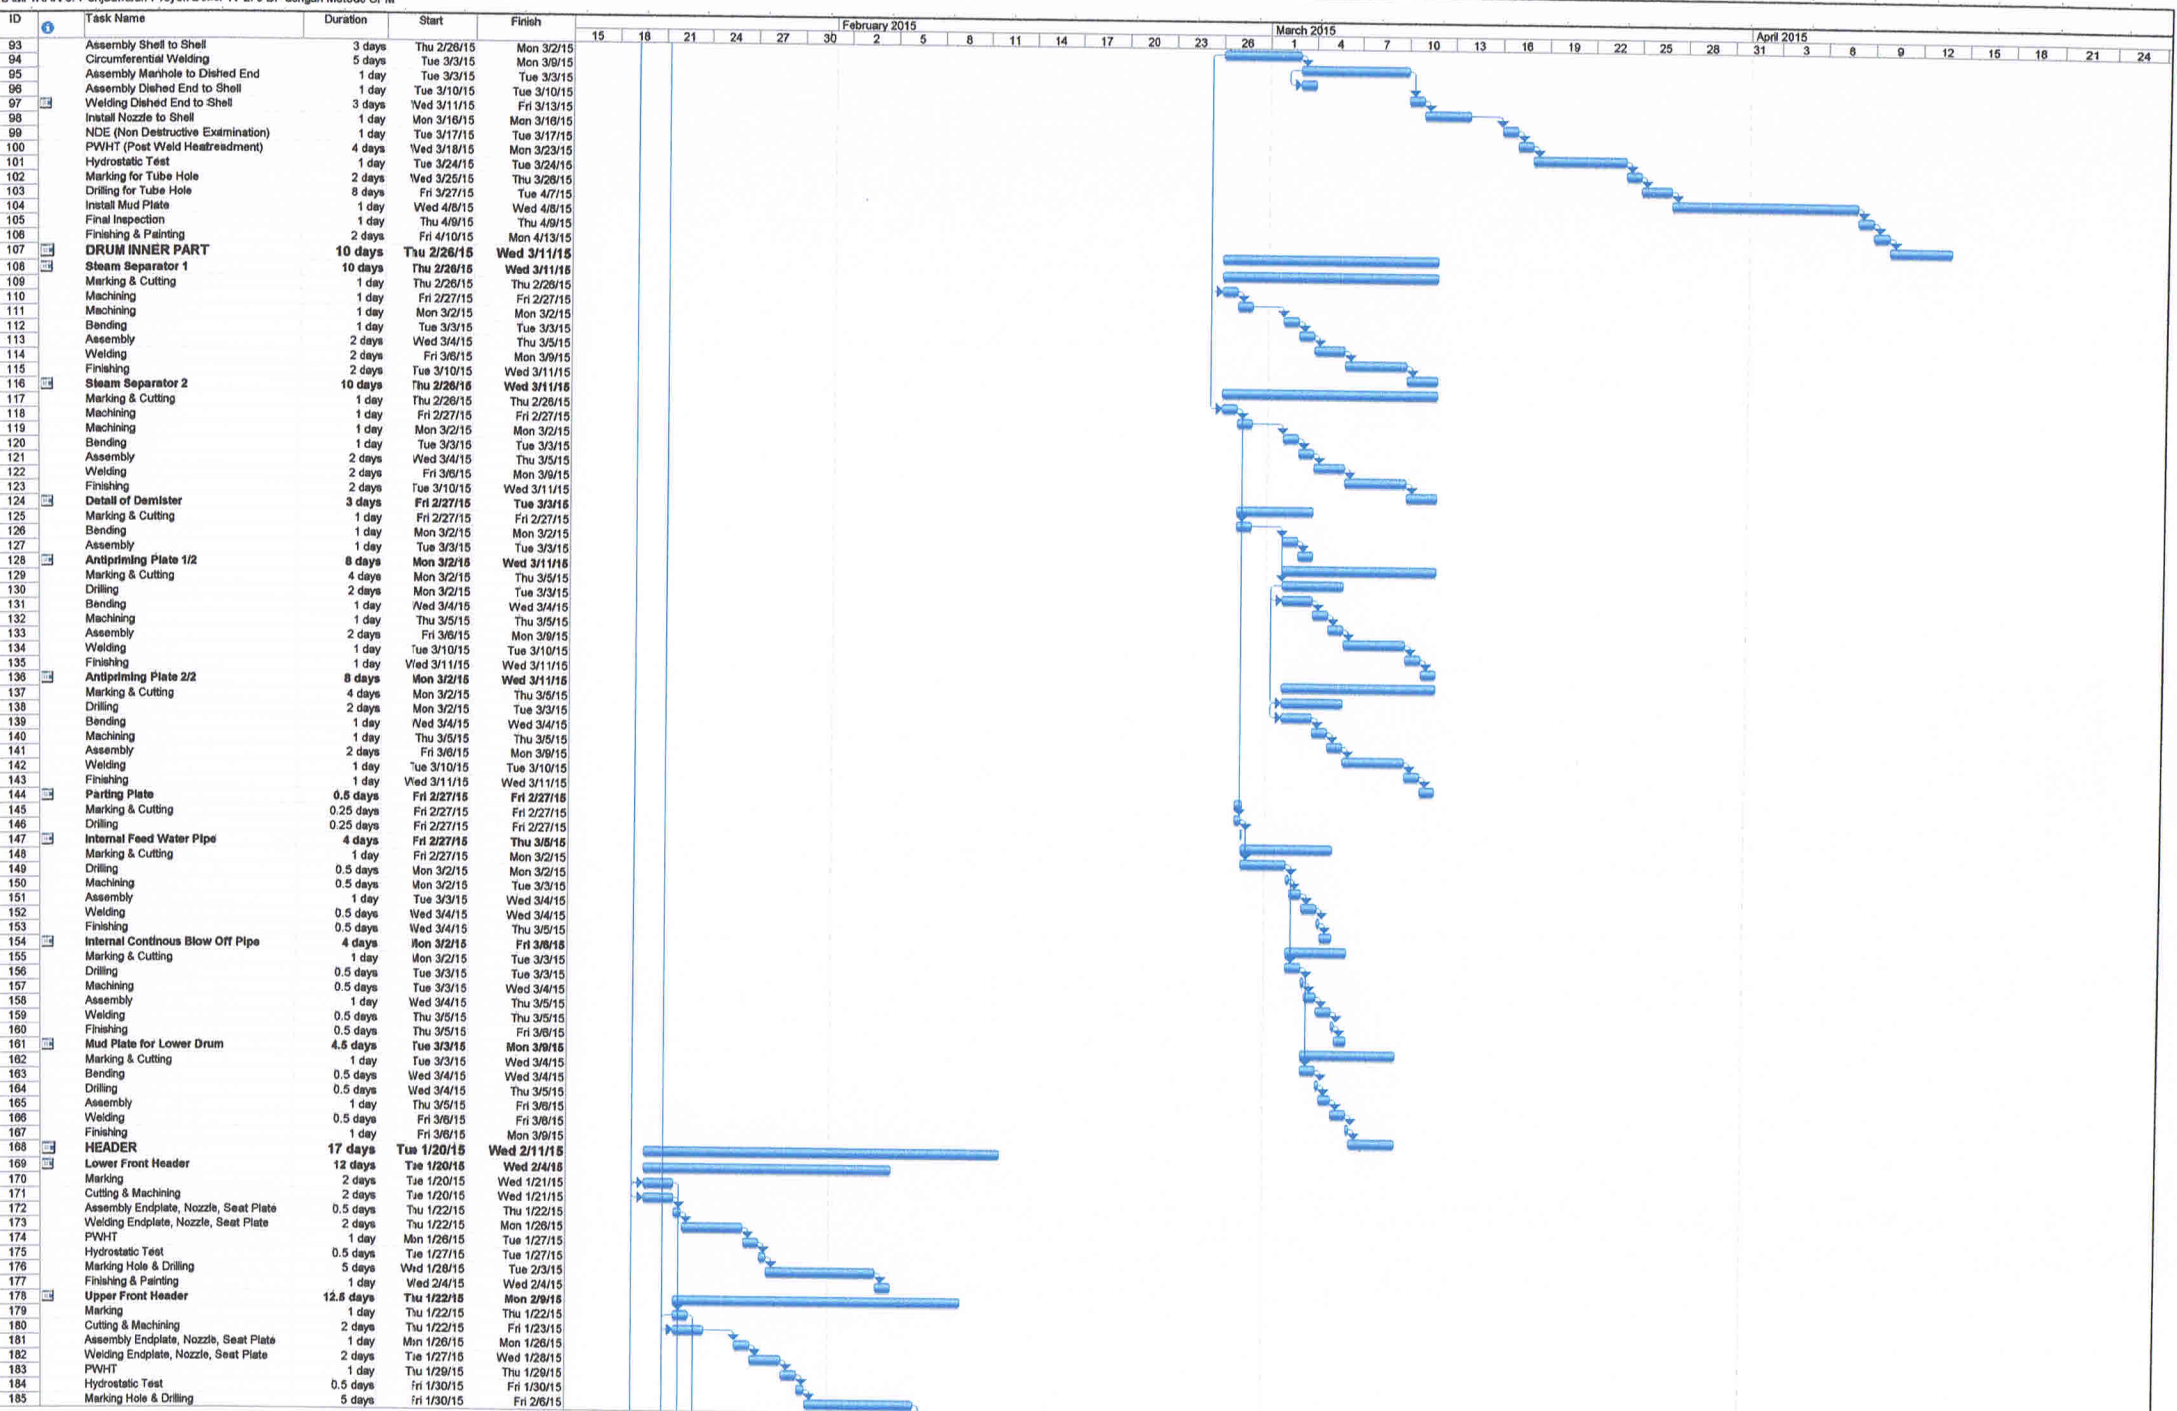

BOILER W-270 DF


Task: Progress (blue bar), Milestone (red diamond), Summary (grey bar), Rolled Up Task (blue bar with diamond), Rolled Up Milestone (red diamond), Rolled Up Critical Task (blue bar with diamond), Rolled Up Progress (red bar), Split (dotted line), External Tasks (grey bar), Project Summary (grey bar), Group By Summary (grey bar), Deadline (grey bar with diamond)

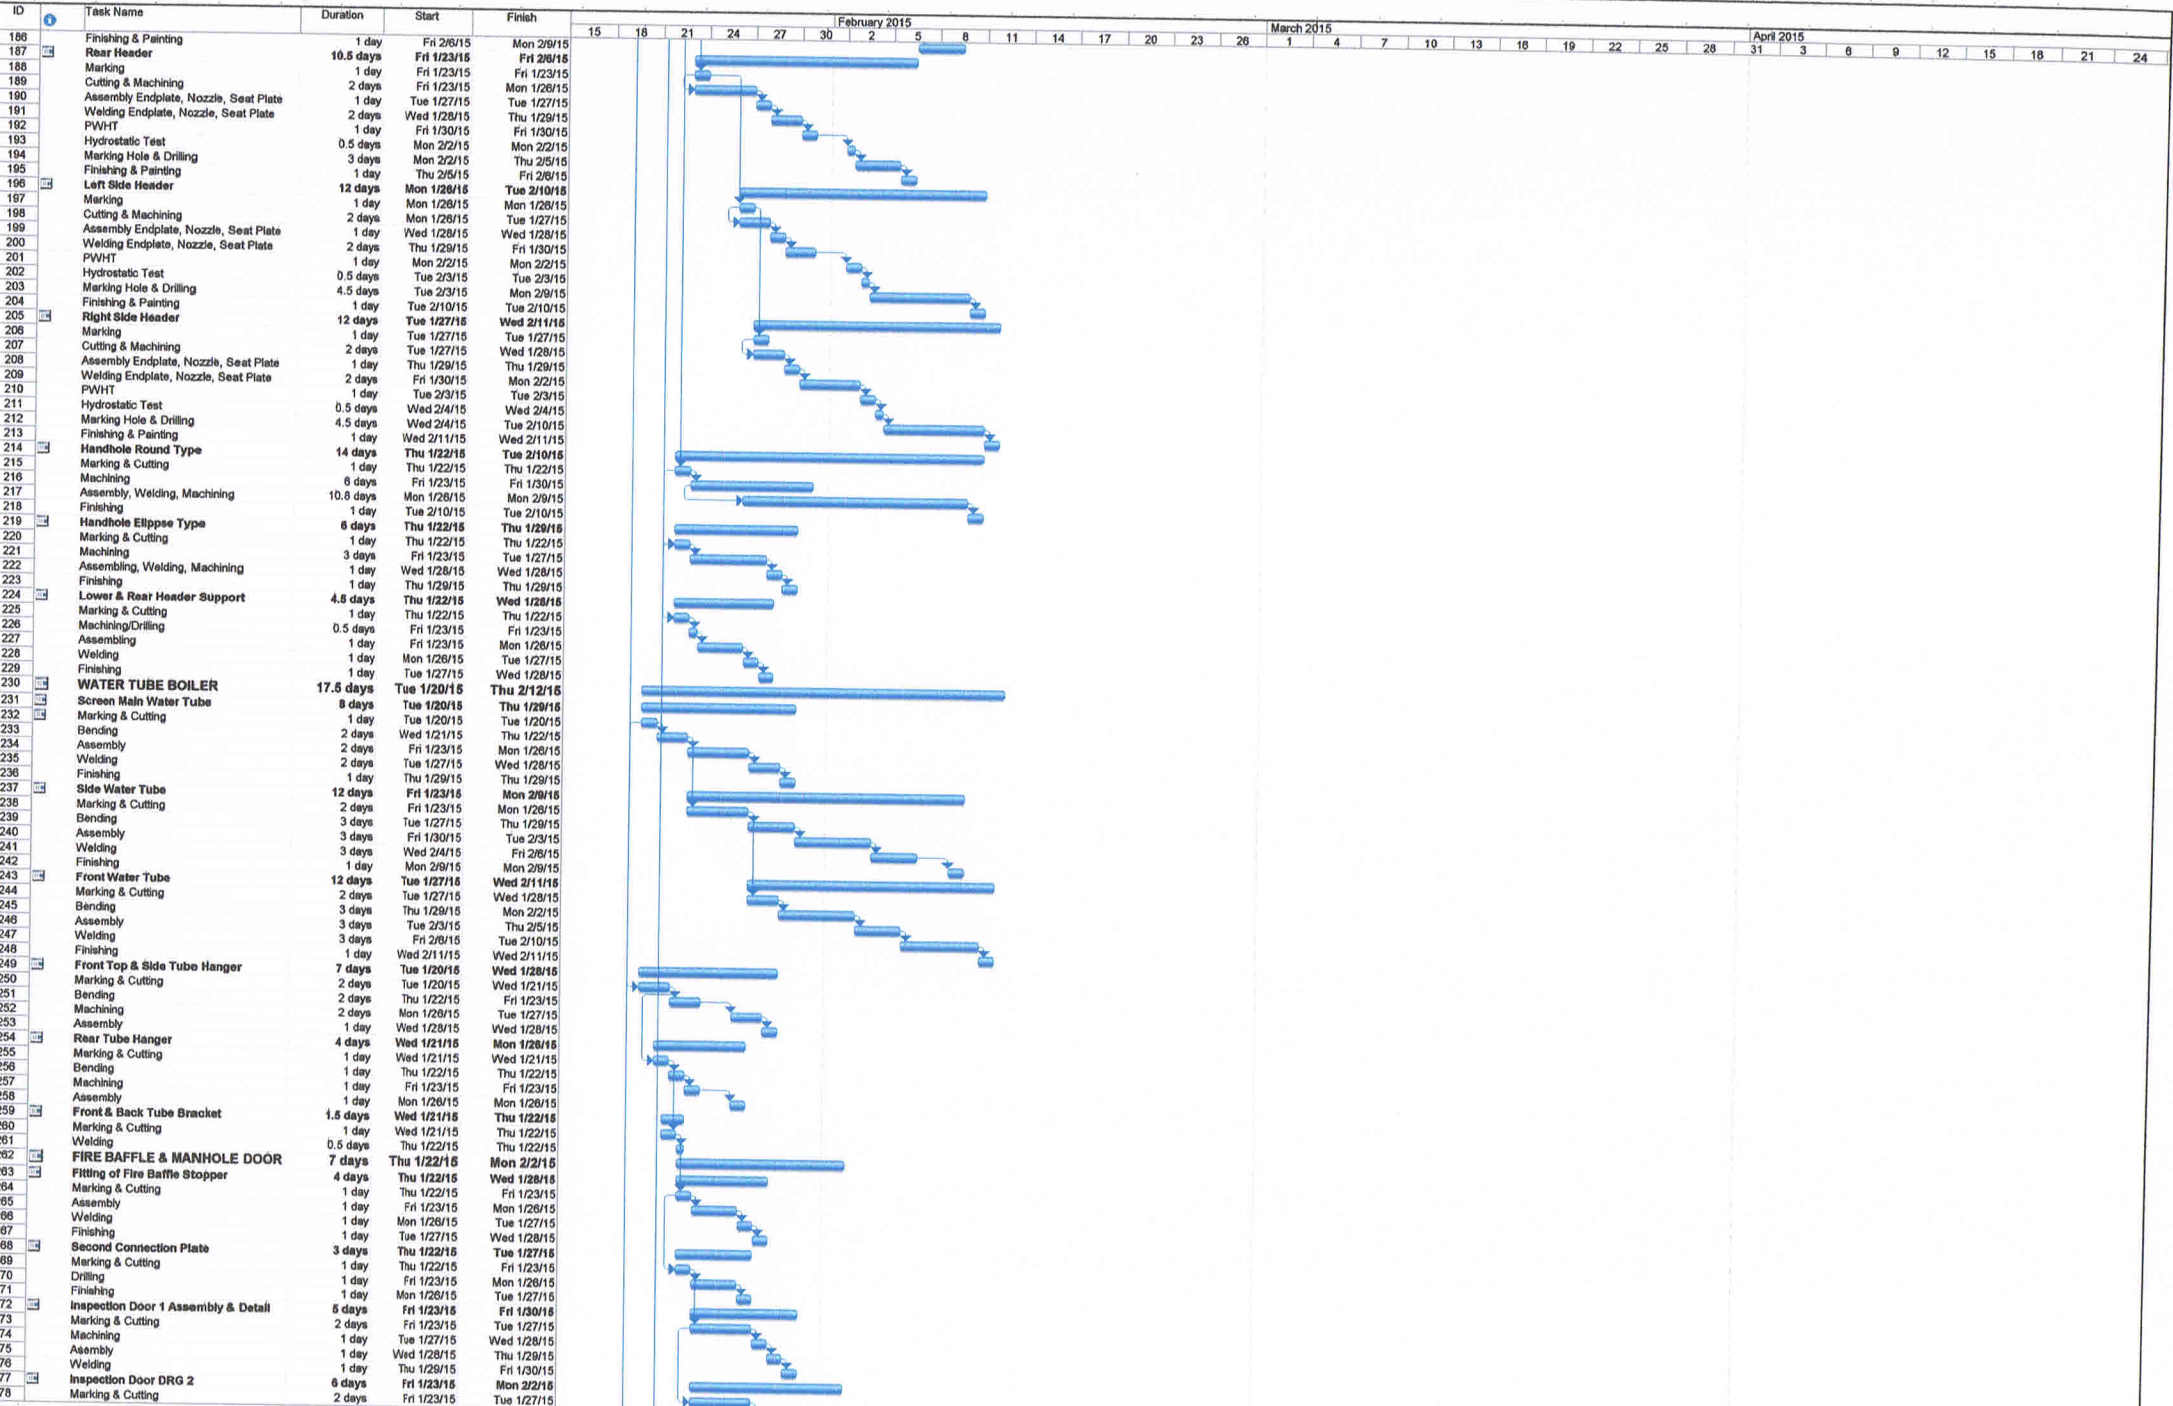


Task Legend: Progress (blue bar), Summary (grey bar), Rolled Up Critical Task (red bar), Rolled Up Progress (red bar with dots), External Tasks (grey bar with dots), Group By Summary (grey bar with arrow), Critical Task (red bar with arrow), Milestone (red diamond), Rolled Up Task (blue bar with arrow), Rolled Up Milestone (red diamond with arrow), Split (grey bar with arrow), Project Summary (grey bar with dots), Deadline (grey bar with arrow).




Task Progress Summary Rolled Up Critical Task Rolled Up Progress External Tasks Group By Summary
Critical Task Milestone Rolled Up Task Rolled Up Milestone Split Project Summary Deadline

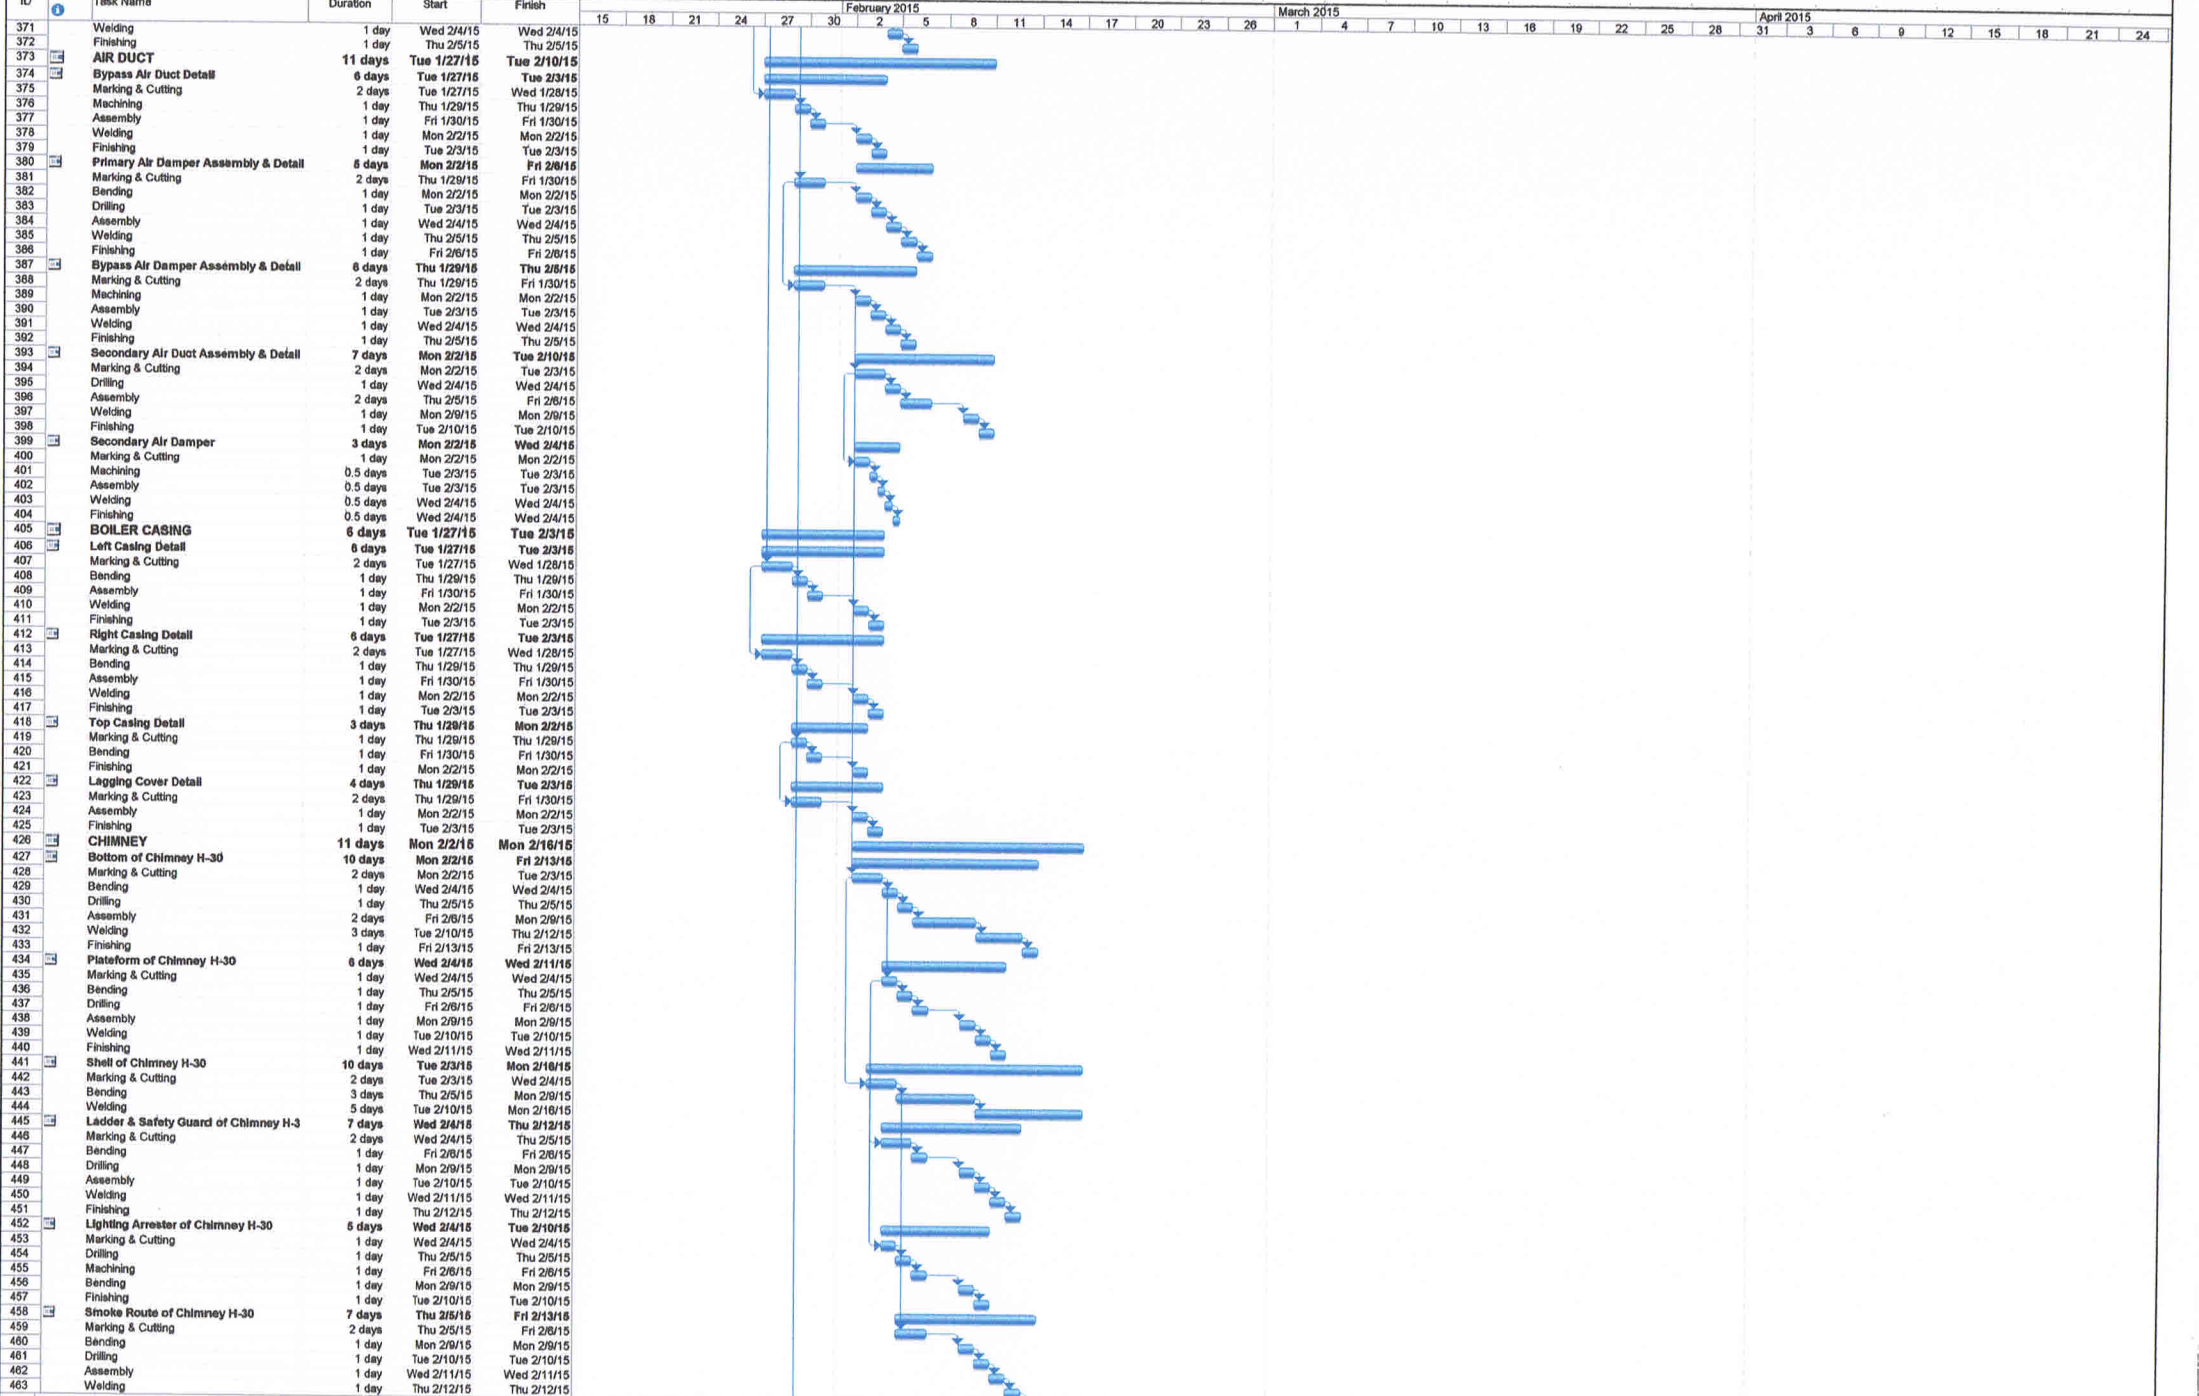

ID	Task Name	Duration	Start	Finish
464	Finishing	1 day	Fri 2/13/15	Fri 2/13/15
465	BLOWN DOWN TANK	6 days	Thu 1/29/15	Thu 2/5/15
466	Marking & Cutting	2 days	Thu 1/29/15	Fri 1/30/15
467	Bending	1 day	Mon 2/2/15	Mon 2/2/15
468	Assembly	1 day	Tue 2/3/15	Tue 2/3/15
469	Welding	1 day	Wed 2/4/15	Wed 2/4/15
470	Finishing	1 day	Thu 2/5/15	Thu 2/5/15




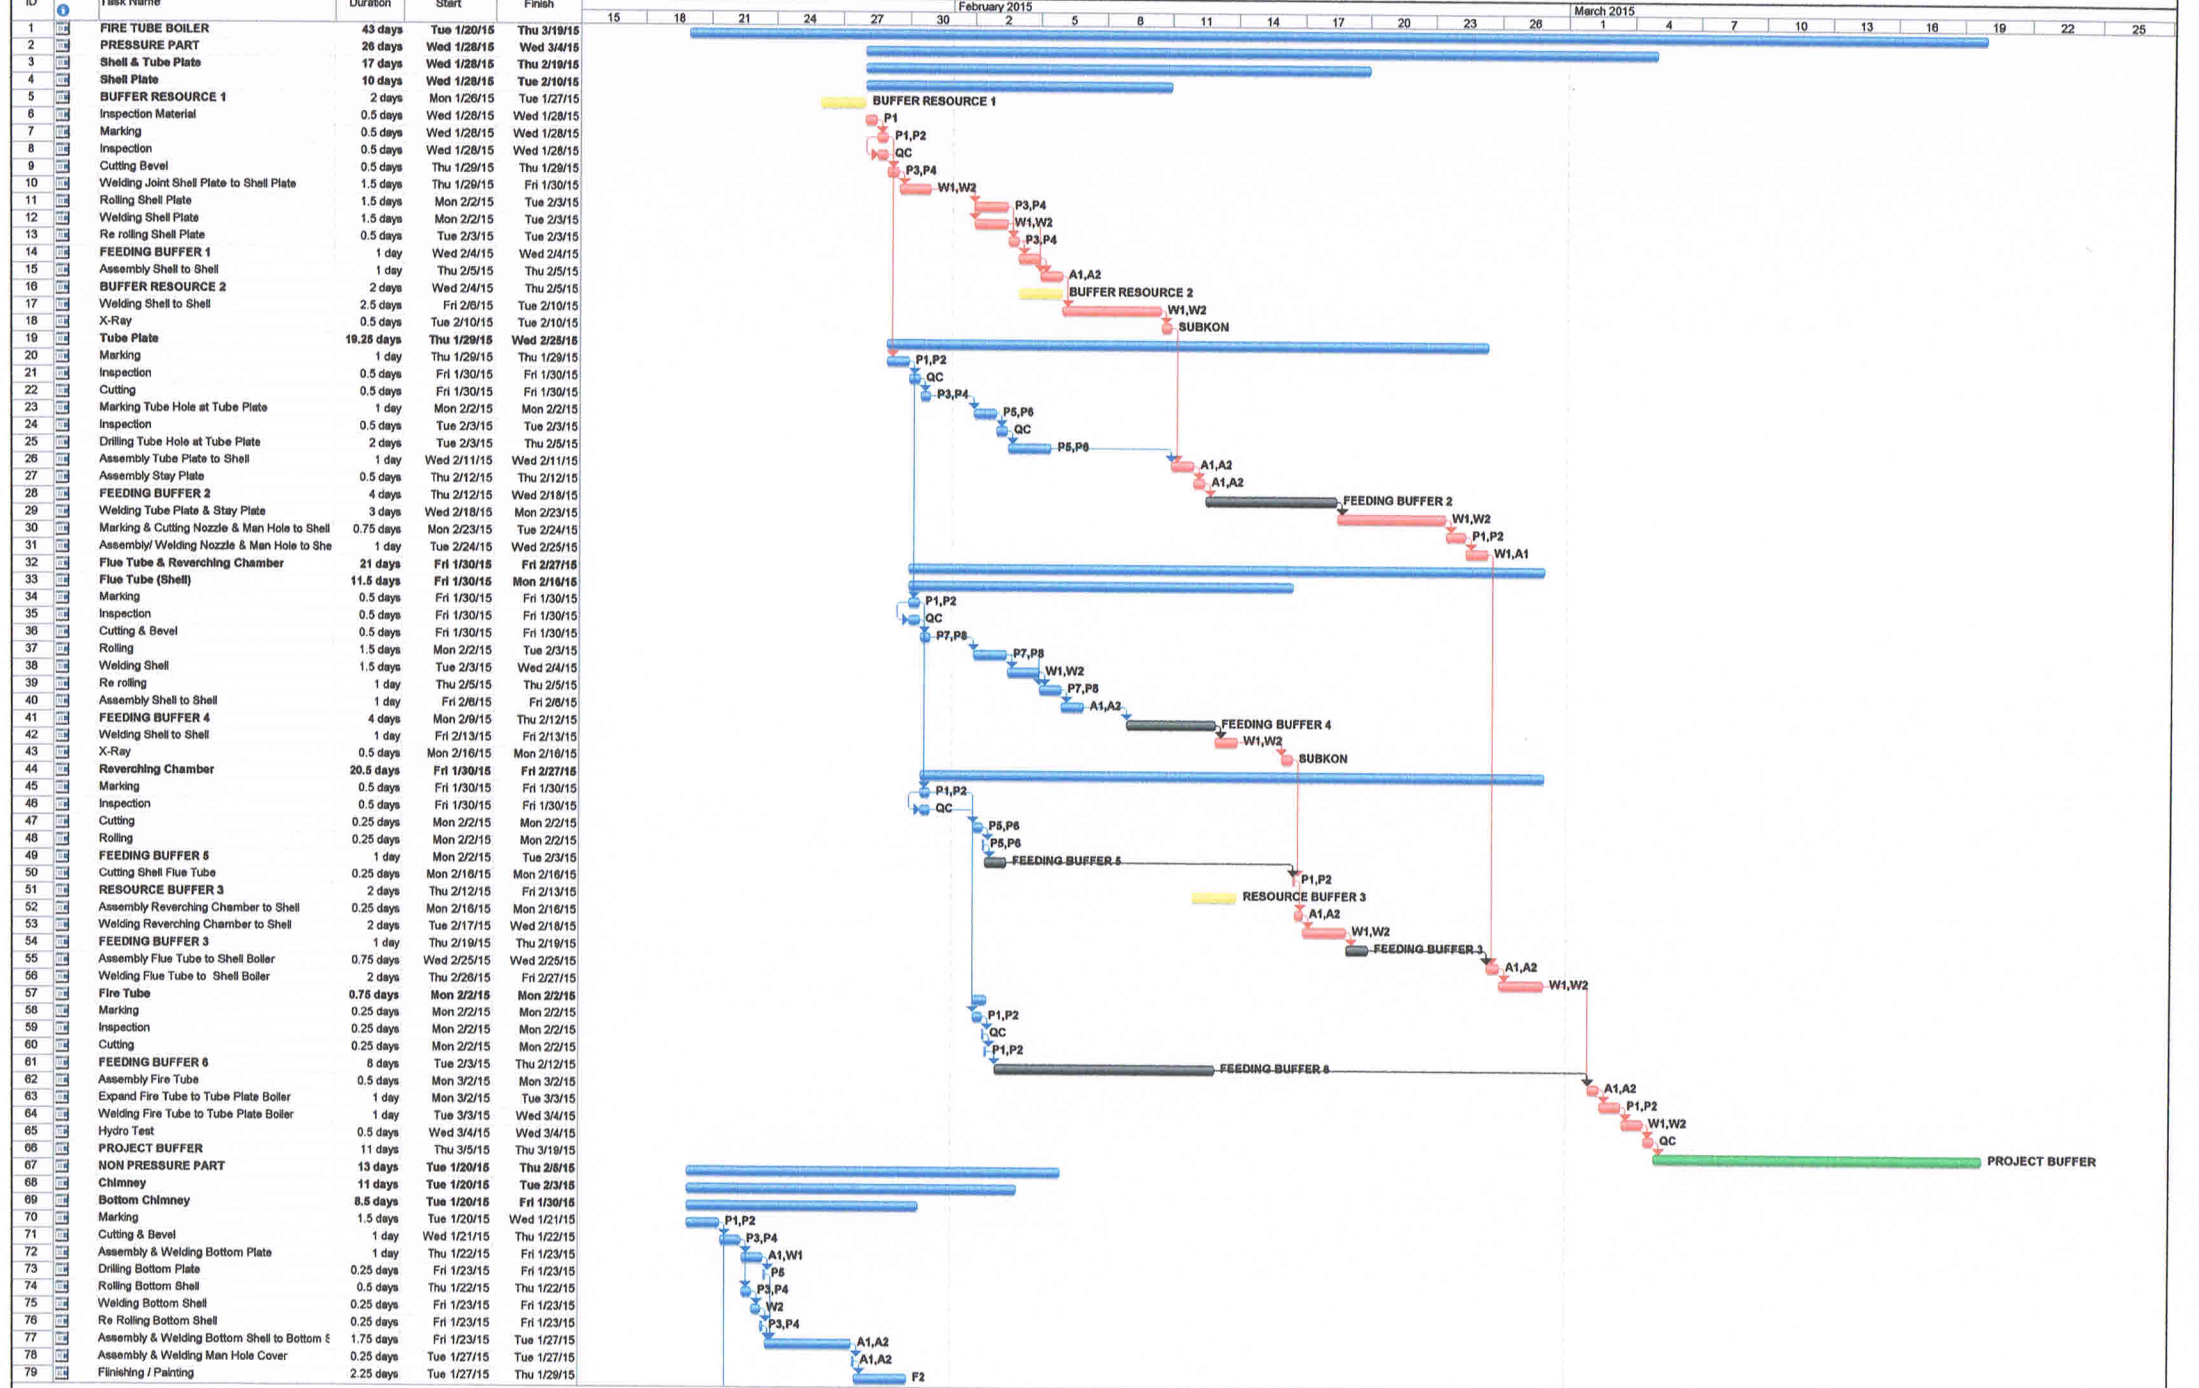

BOILER F-80 L


Task: Progress (blue bar), Milestone (red diamond), Summary (grey bar), Rolled Up Task (blue bar with diamond), Rolled Up Milestone (red diamond with circle), Rolled Up Progress (red bar with diamond), Split (grey bar with diamond), External Tasks (grey bar), Project Summary (grey bar with diamond), Group By Summary (grey bar with diamond), Deadline (grey bar with diamond)


Page 1

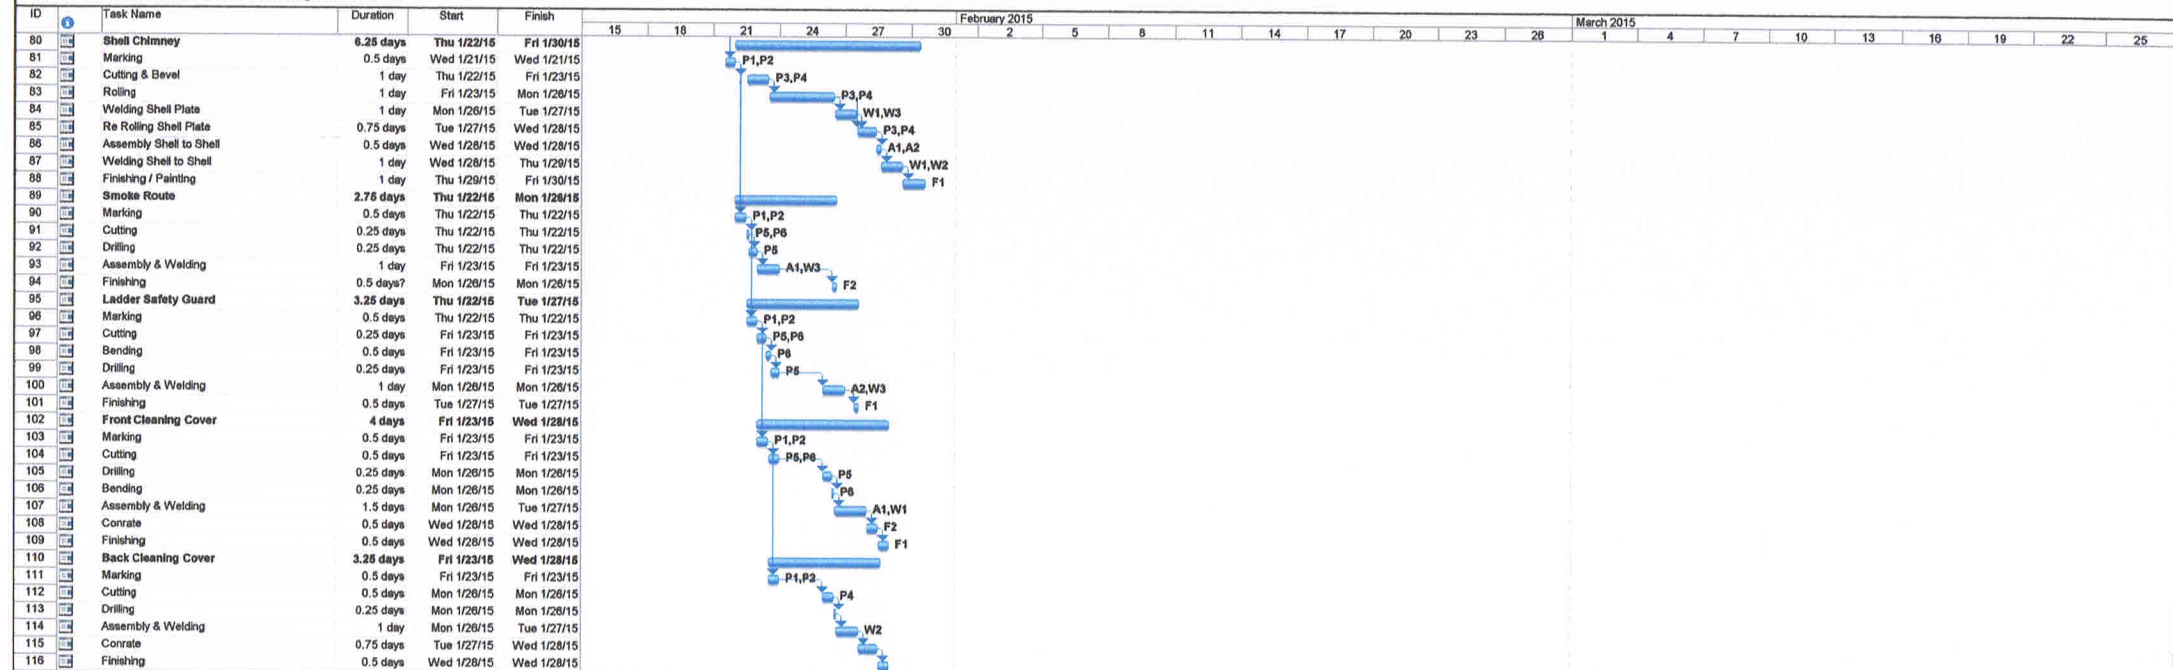


BOILER F-80 L

- Task: Progress (blue bar), Milestone (red bar)
- Critical Task: (red bar)
- Summary: (grey bar)
- Rolled Up Task: (blue bar)
- Rolled Up Critical Task: (red bar)
- Rolled Up Milestone: (red bar)
- Rolled Up Progress: (red bar)
- External Tasks: (grey bar)
- Project Summary: (grey bar)
- Group By Summary: (grey bar)
- Deadline: (grey bar)
- Split: (dotted line)

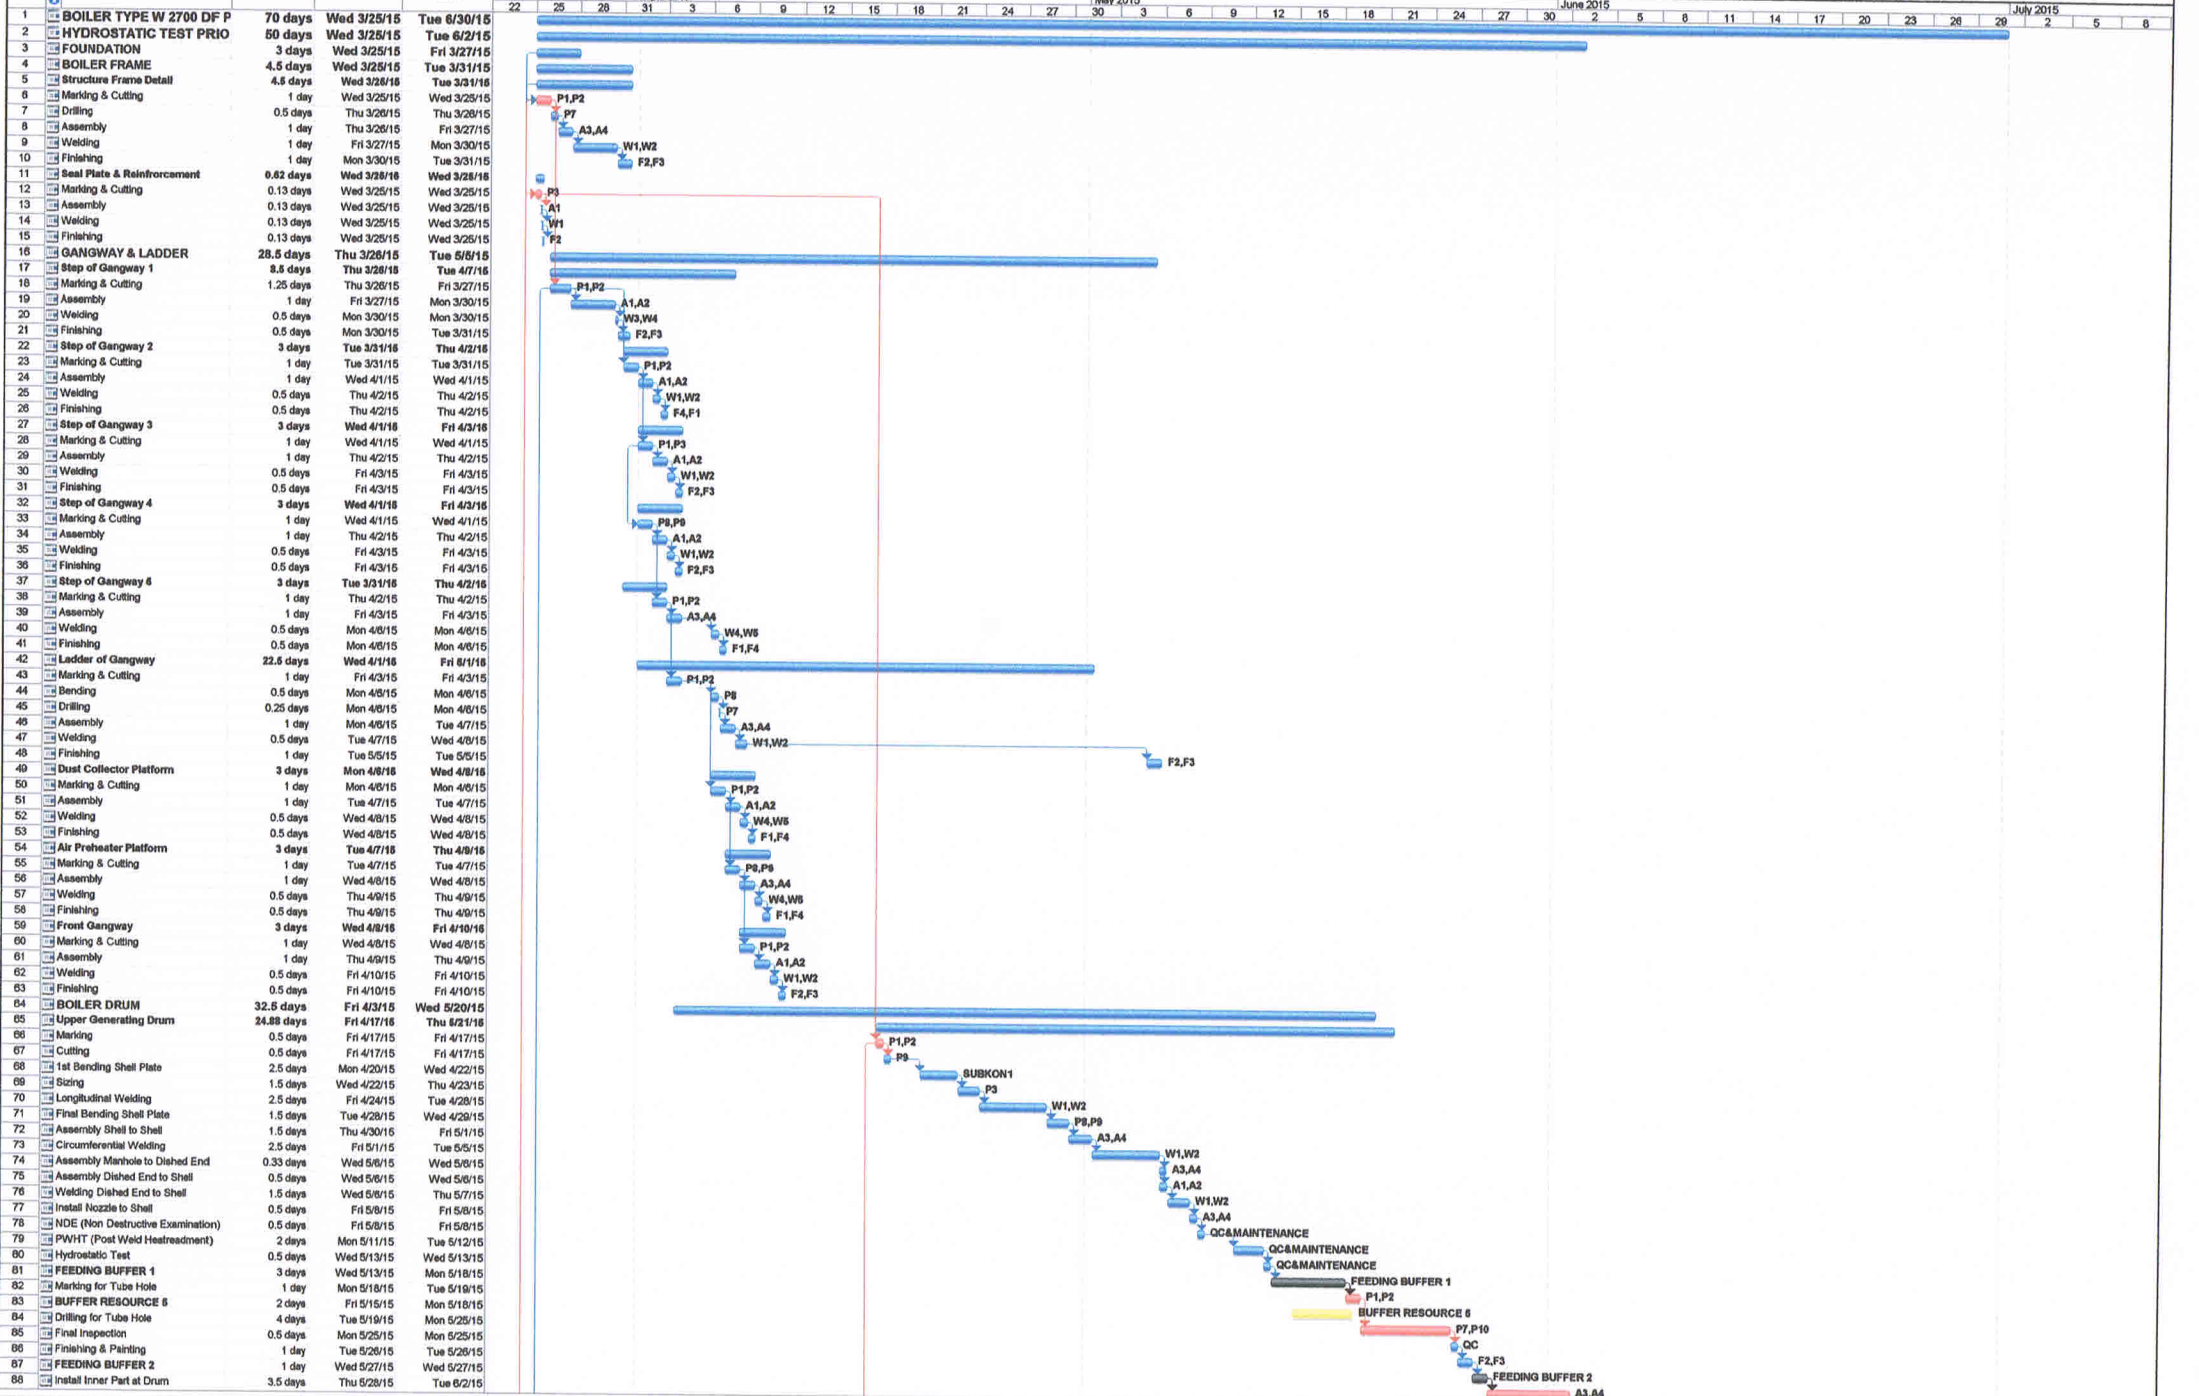


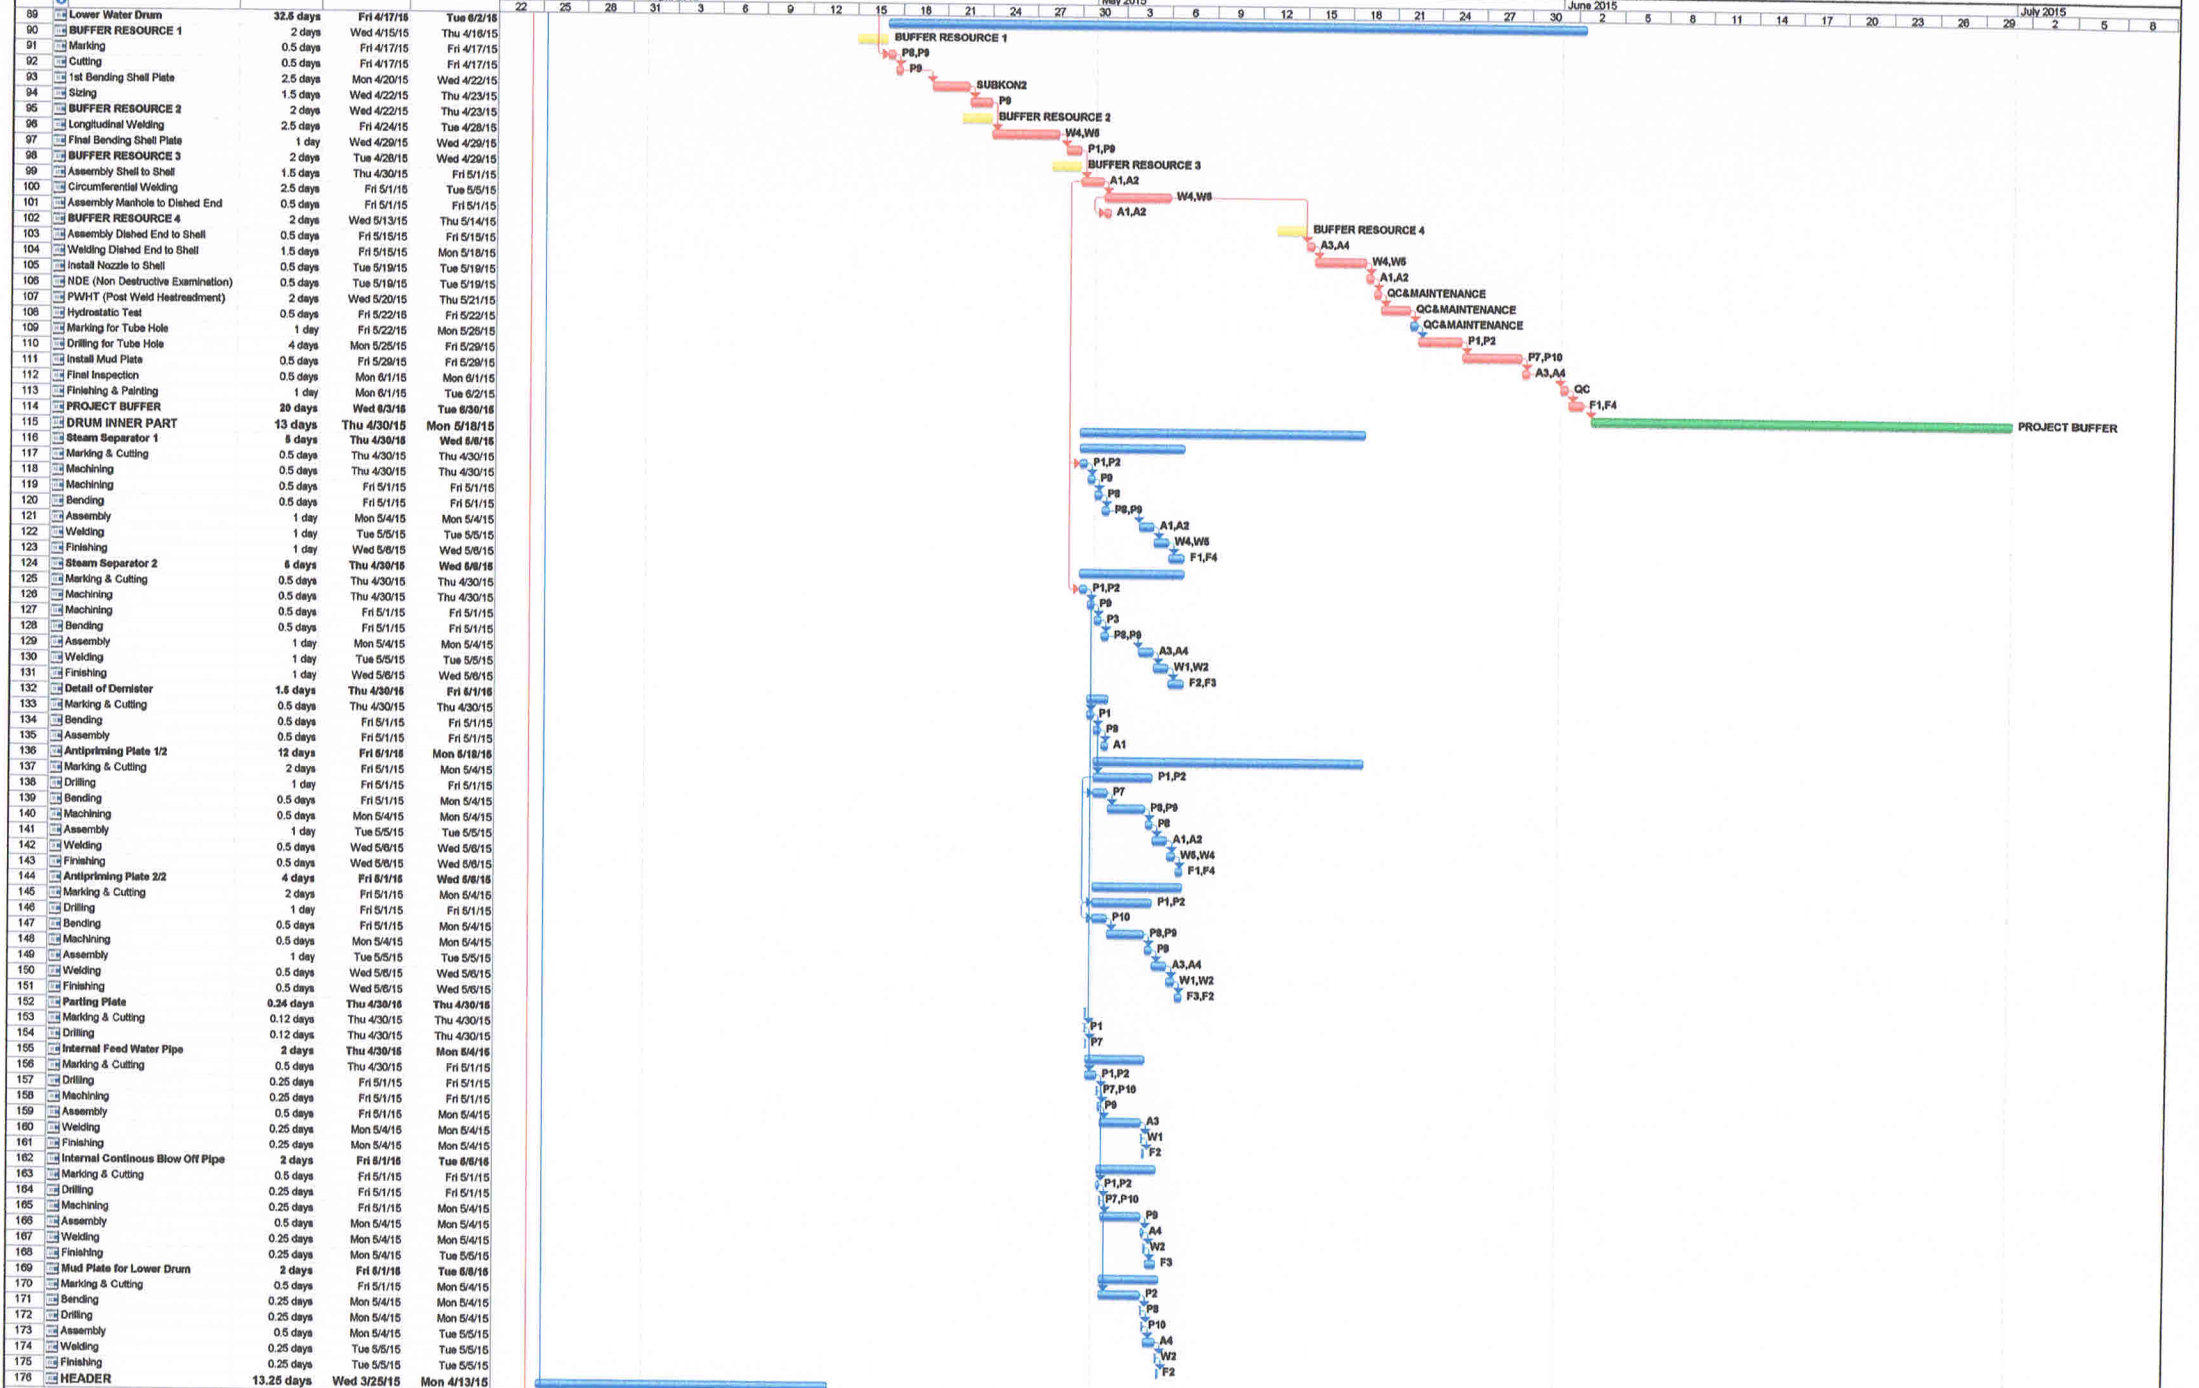

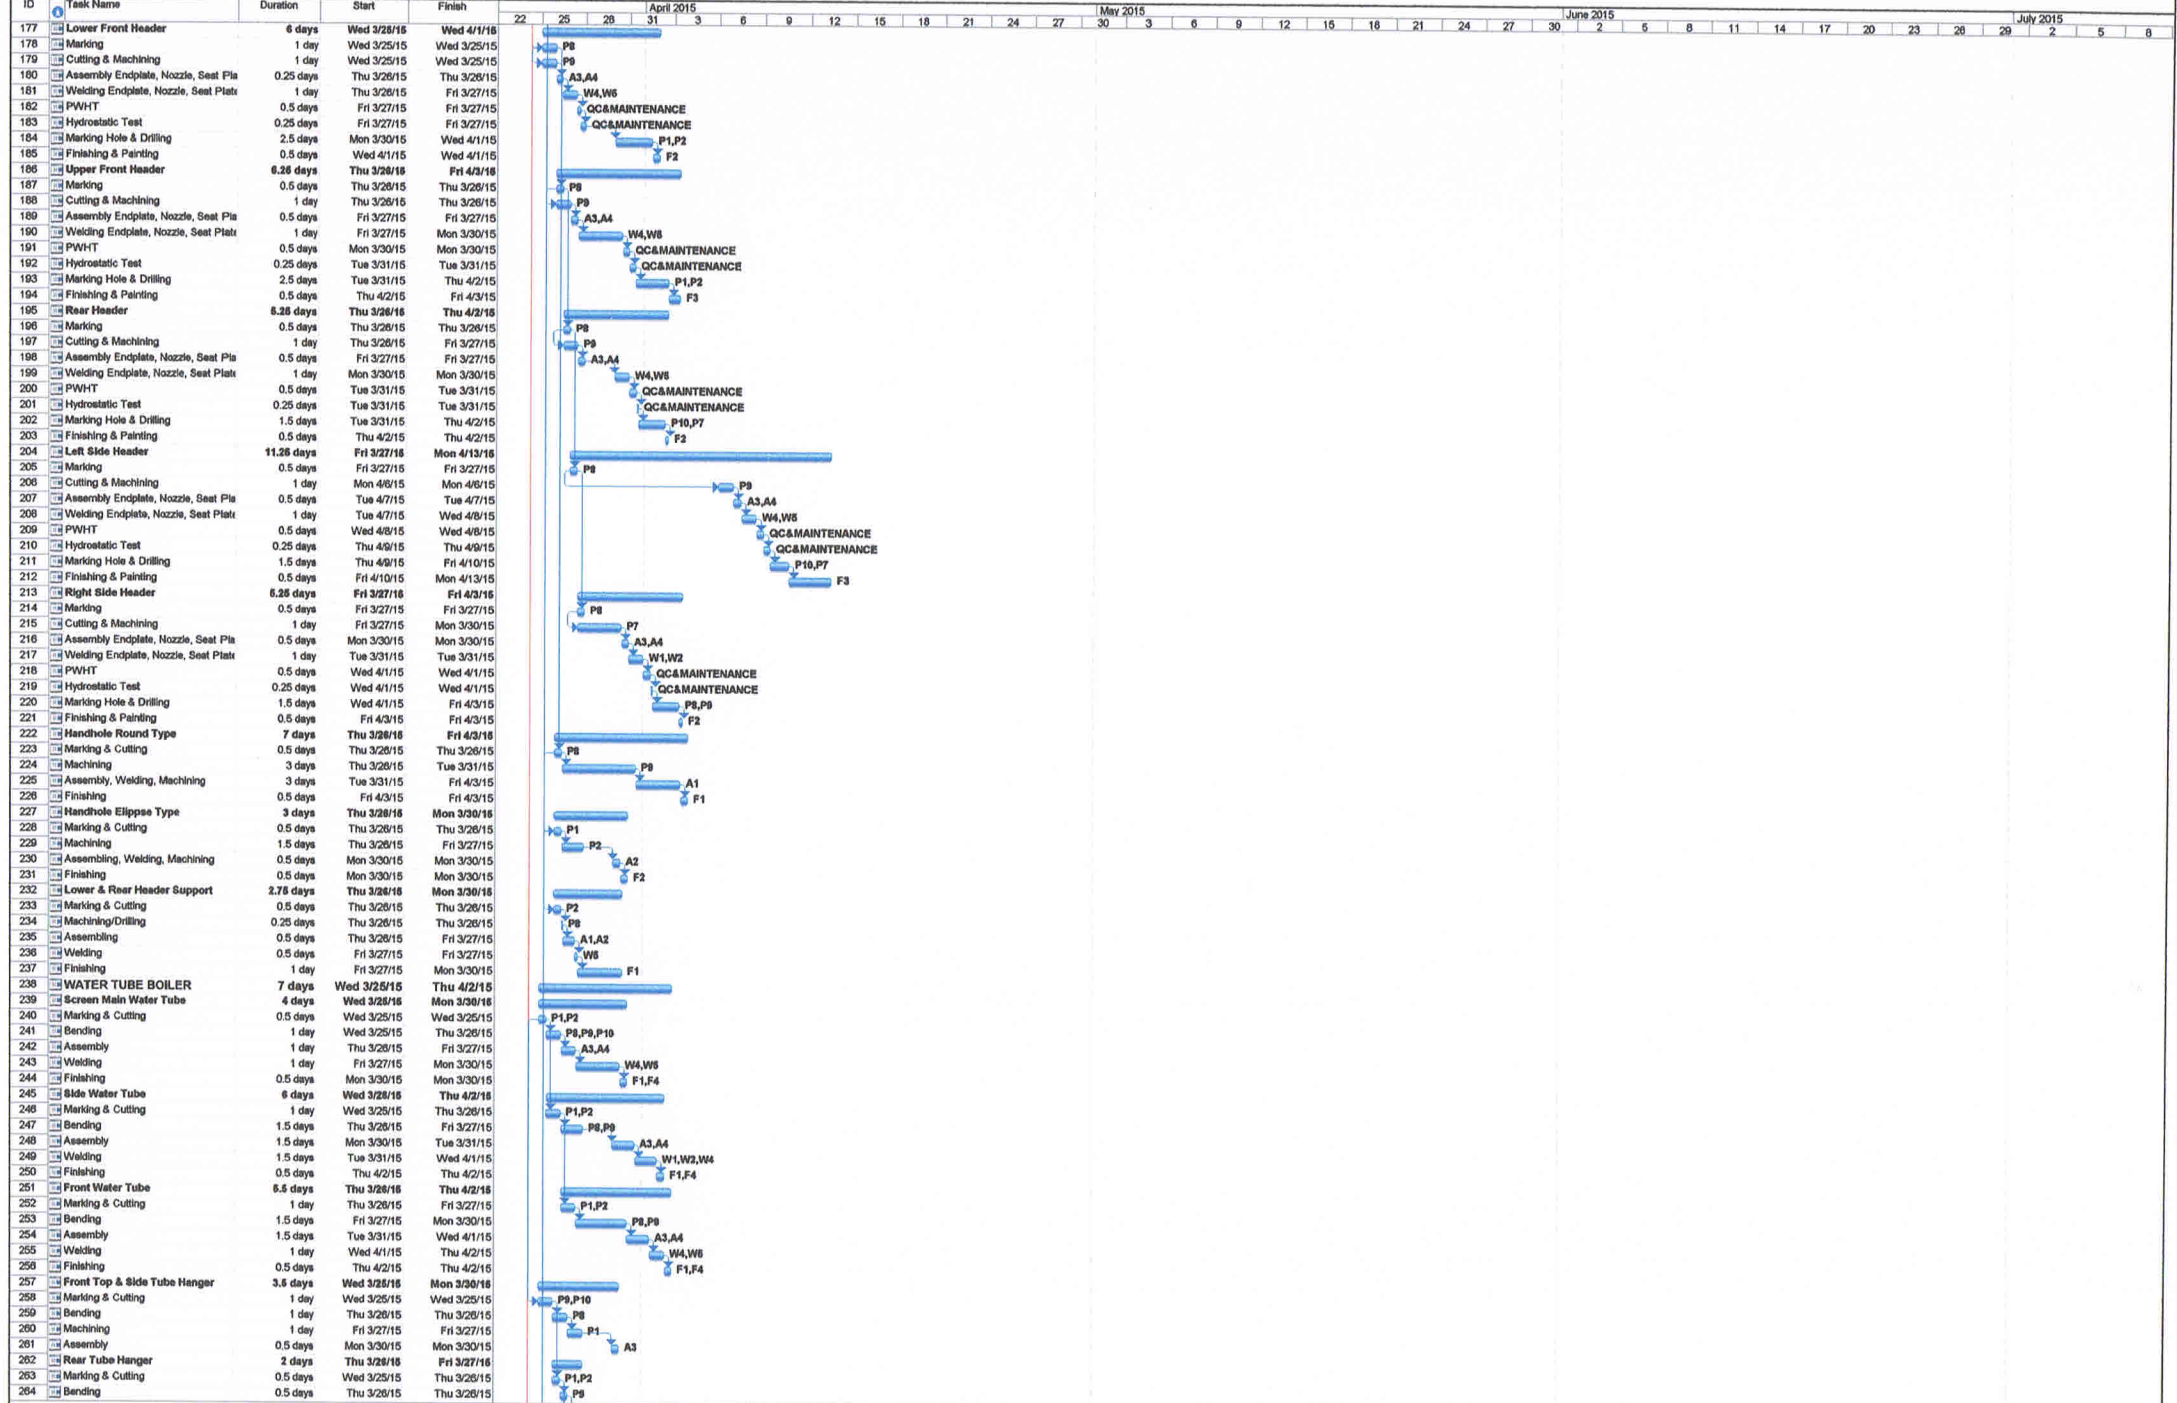

Project: Boiler W-270 DF


Task Progress Summary Rolled Up Critical Task Rolled Up Progress External Tasks Group By Summary
Critical Task Milestone Rolled Up Task Rolled Up Milestone Split Project Summary Deadline

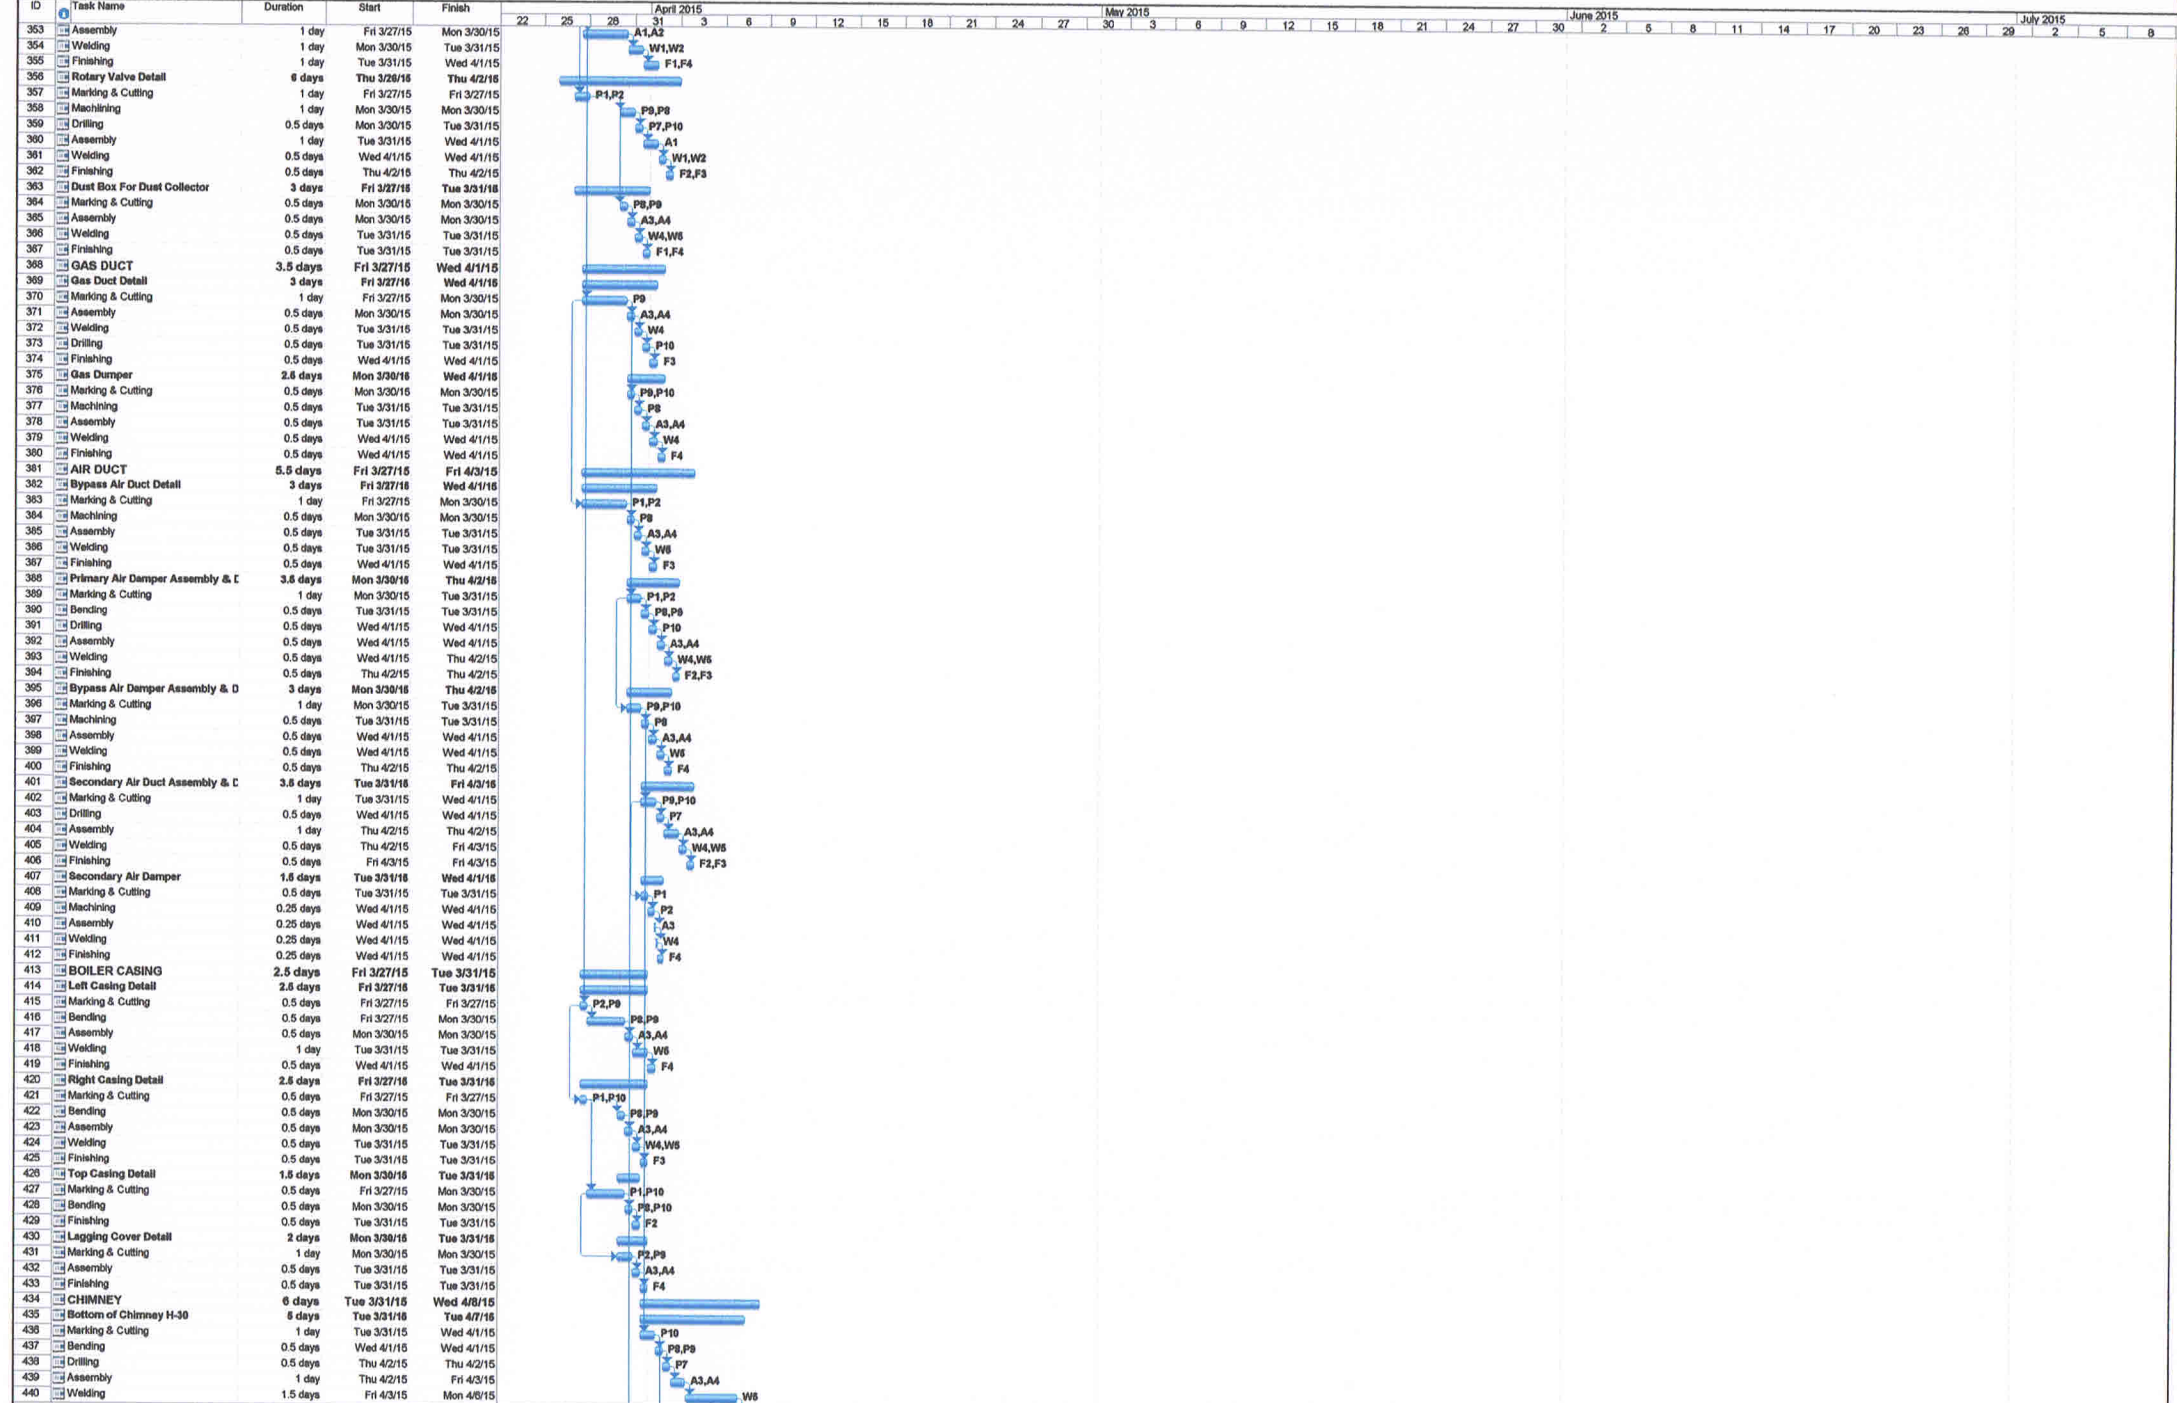


Project: Boiler W-270 DF

Task Progress Summary Rolled Up Critical Task Rolled Up Progress External Tasks Group By Summary
Critical Task Milestone Rolled Up Task Rolled Up Milestone Split Project Summary Deadline


ID	Task Name	Duration	Start	Finish
441	Finishing	0.5 days	Tue 4/7/15	Tue 4/7/15
442	Platform of Chimney H-30	3 days	Wed 4/1/15	Mon 4/6/15
443	Marking & Cutting	0.5 days	Wed 4/1/15	Wed 4/1/15
444	Bending	0.5 days	Thu 4/2/15	Thu 4/2/15
445	Drilling	0.5 days	Thu 4/2/15	Thu 4/2/15
446	Assembly	0.5 days	Fri 4/3/15	Fri 4/3/15
447	Welding	0.5 days	Fri 4/3/15	Fri 4/3/15
448	Finishing	0.5 days	Mon 4/6/15	Mon 4/6/15
449	Shell of Chimney H-30	5 days	Wed 4/1/15	Wed 4/8/15
450	Marking & Cutting	1 day	Wed 4/1/15	Thu 4/2/15
451	Bending	1.5 days	Thu 4/2/15	Fri 4/3/15
452	Welding	2.5 days	Mon 4/6/15	Wed 4/8/15
453	Ladder & Safety Guard of Chimney	3.5 days	Wed 4/1/15	Mon 4/6/15
454	Marking & Cutting	1 day	Wed 4/1/15	Thu 4/2/15
455	Bending	0.5 days	Thu 4/2/15	Thu 4/2/15
456	Drilling	0.5 days	Fri 4/3/15	Fri 4/3/15
457	Assembly	0.5 days	Fri 4/3/15	Fri 4/3/15
458	Welding	0.5 days	Mon 4/6/15	Mon 4/6/15
459	Finishing	0.5 days	Mon 4/6/15	Mon 4/6/15
460	Lighting Arrester of Chimney H-30	2.5 days	Wed 4/1/15	Fri 4/3/15
461	Marking & Cutting	0.5 days	Wed 4/1/15	Wed 4/1/15
462	Drilling	0.5 days	Thu 4/2/15	Thu 4/2/15
463	Machining	0.5 days	Thu 4/2/15	Thu 4/2/15
464	Bending	0.5 days	Fri 4/3/15	Fri 4/3/15
465	Finishing	0.5 days	Fri 4/3/15	Fri 4/3/15
466	Smoke Route of Chimney H-30	3.5 days	Thu 4/2/15	Tue 4/7/15
467	Marking & Cutting	1 day	Thu 4/2/15	Fri 4/3/15
468	Bending	0.5 days	Fri 4/3/15	Fri 4/3/15
469	Drilling	0.5 days	Mon 4/6/15	Mon 4/6/15
470	Assembly	0.5 days	Mon 4/6/15	Mon 4/6/15
471	Welding	0.5 days	Tue 4/7/15	Tue 4/7/15
472	Finishing	0.5 days	Tue 4/7/15	Tue 4/7/15
473	BLOWN DOWN TANK	3 days	Mon 3/30/15	Thu 4/2/15
474	Marking & Cutting	1 day	Mon 3/30/15	Tue 3/31/15
475	Bending	0.5 days	Tue 3/31/15	Tue 3/31/15
476	Assembly	0.5 days	Wed 4/1/15	Wed 4/1/15
477	Welding	0.5 days	Wed 4/1/15	Wed 4/1/15
478	Finishing	0.5 days	Thu 4/2/15	Thu 4/2/15

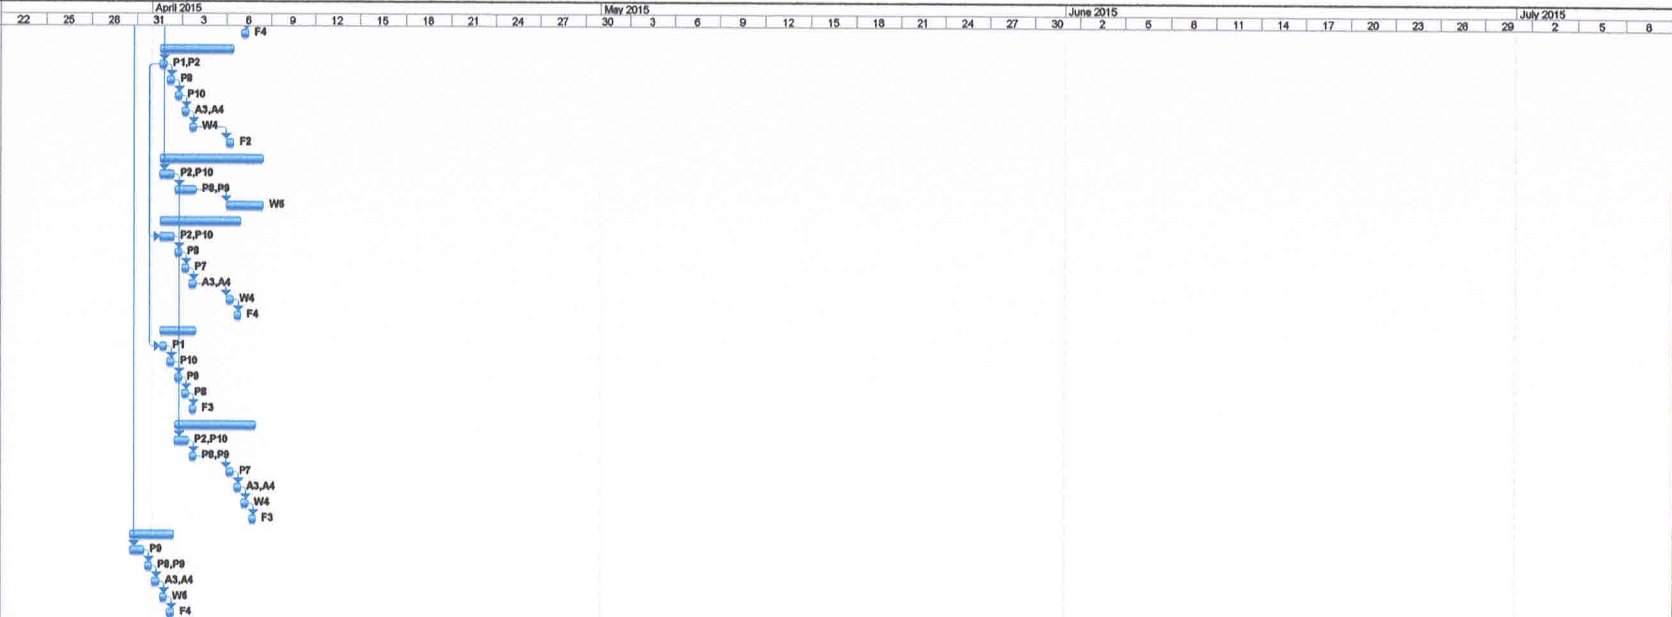

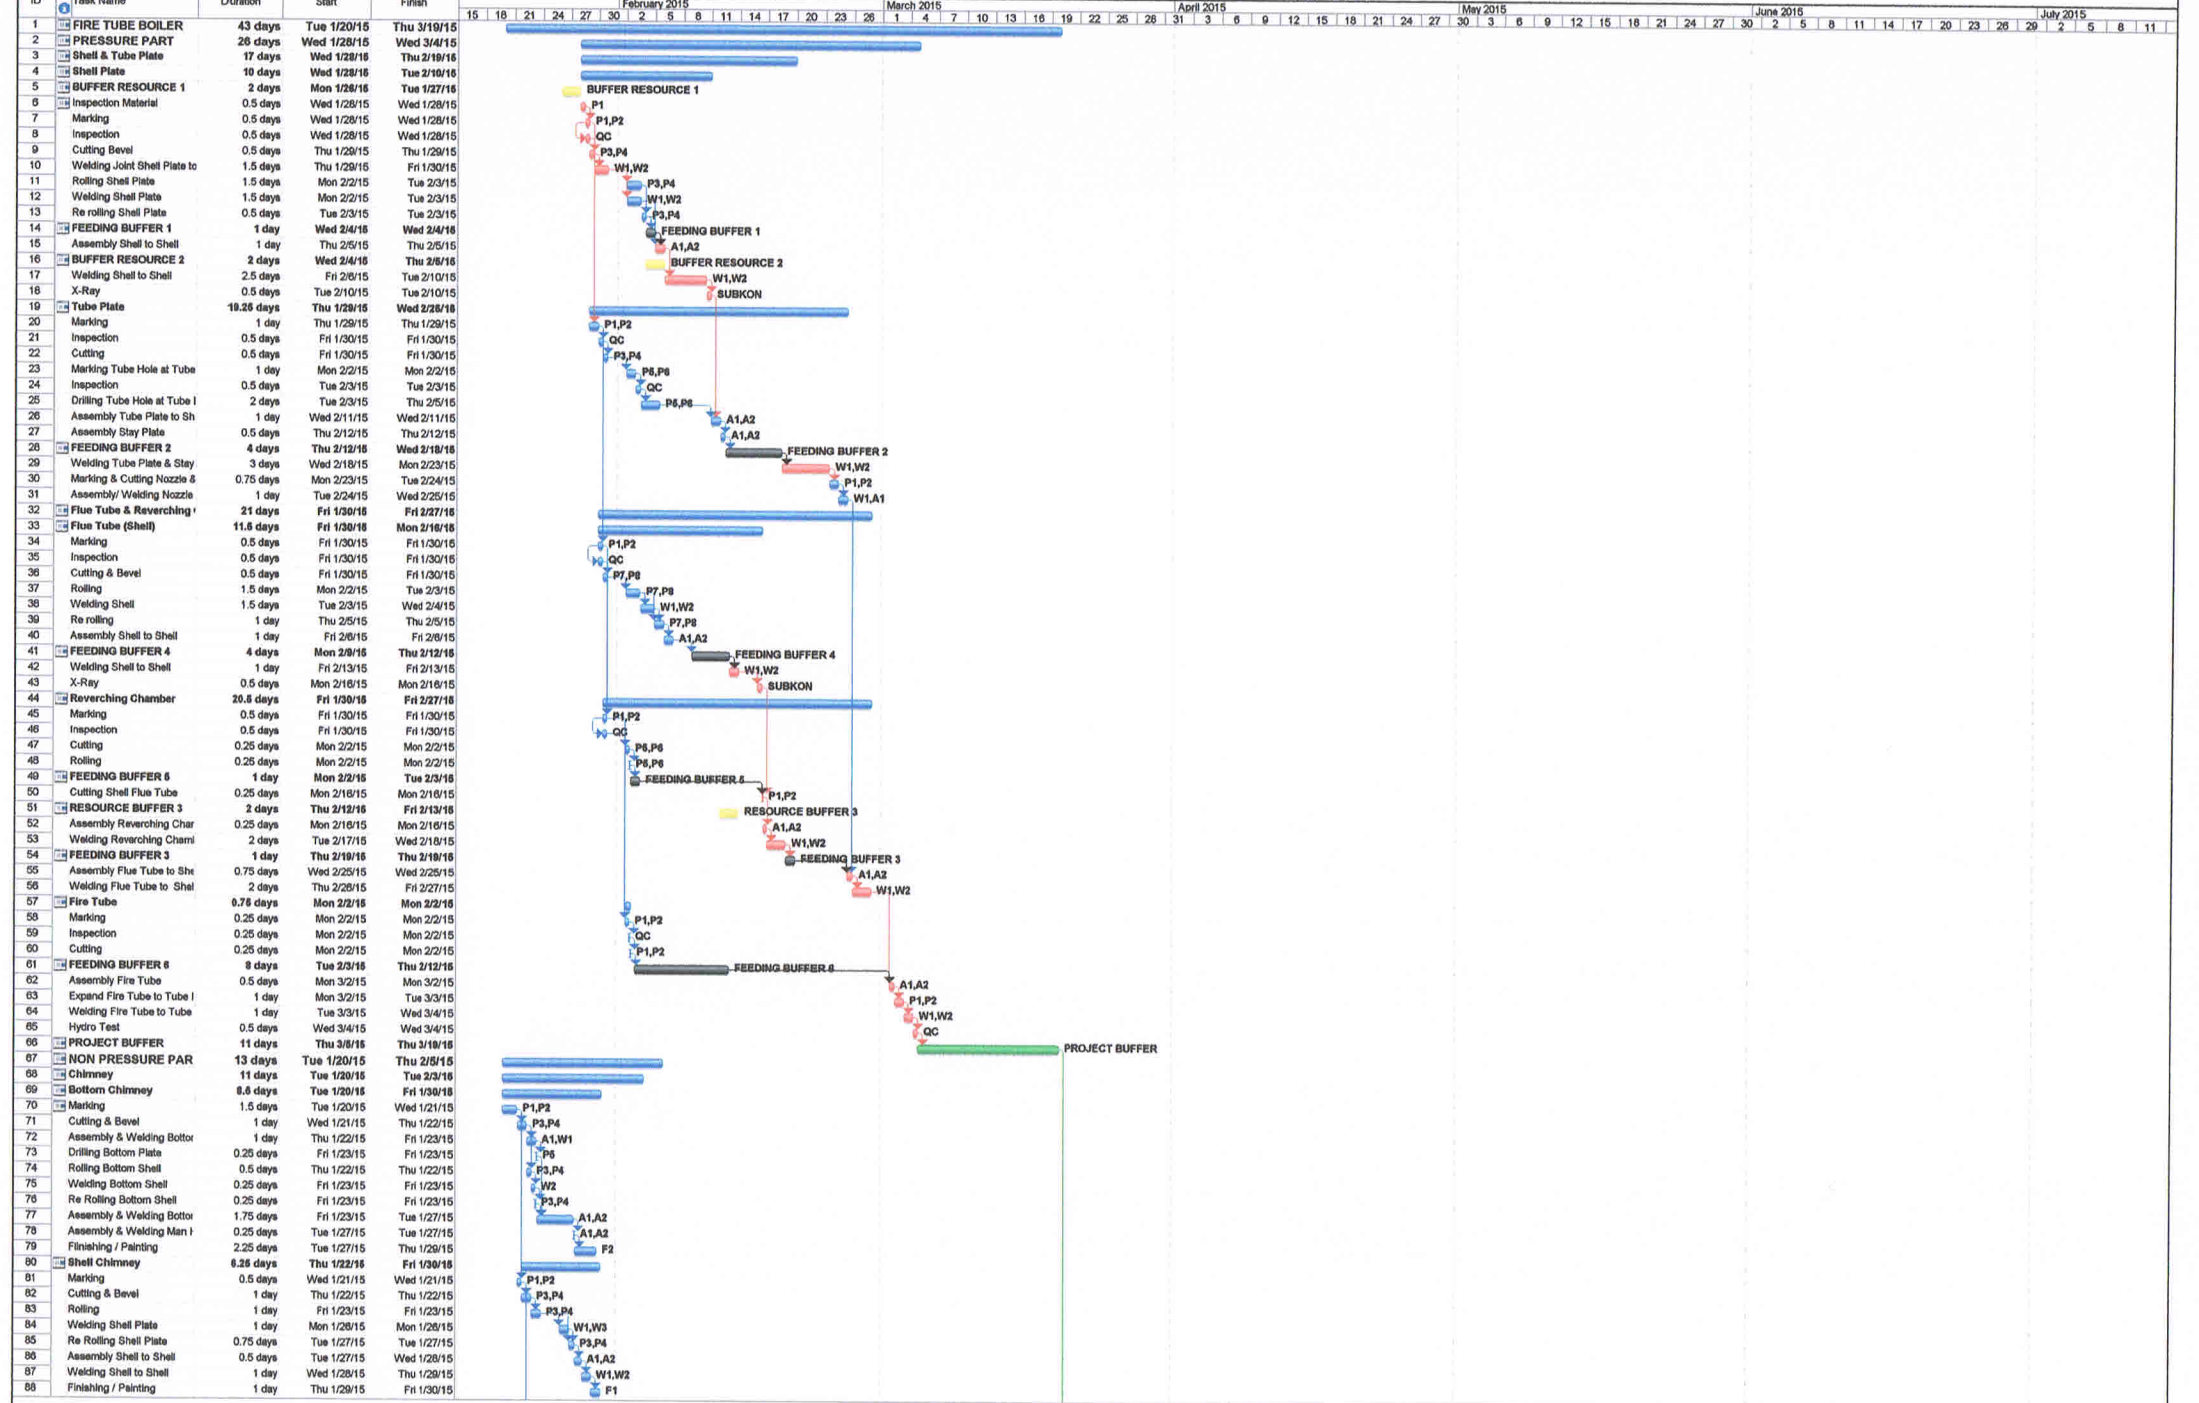

Project: Fire Tube F-80 L dan Water T


Task Legend: Progress (Blue bar), Summary (Grey bar), Rolled Up Critical Task (Red bar), External Tasks (Light Blue bar), Group By Summary (Dashed line), Critical Task (Red bar with diamond), Milestone (Red diamond), Rolled Up Task (Blue bar with diamond), Rolled Up Milestone (Red diamond with diamond), Rolled Up Progress (Red bar with diamond), Split (Dashed line), Project Summary (Grey bar with diamond), Deadline (Dashed line with diamond).

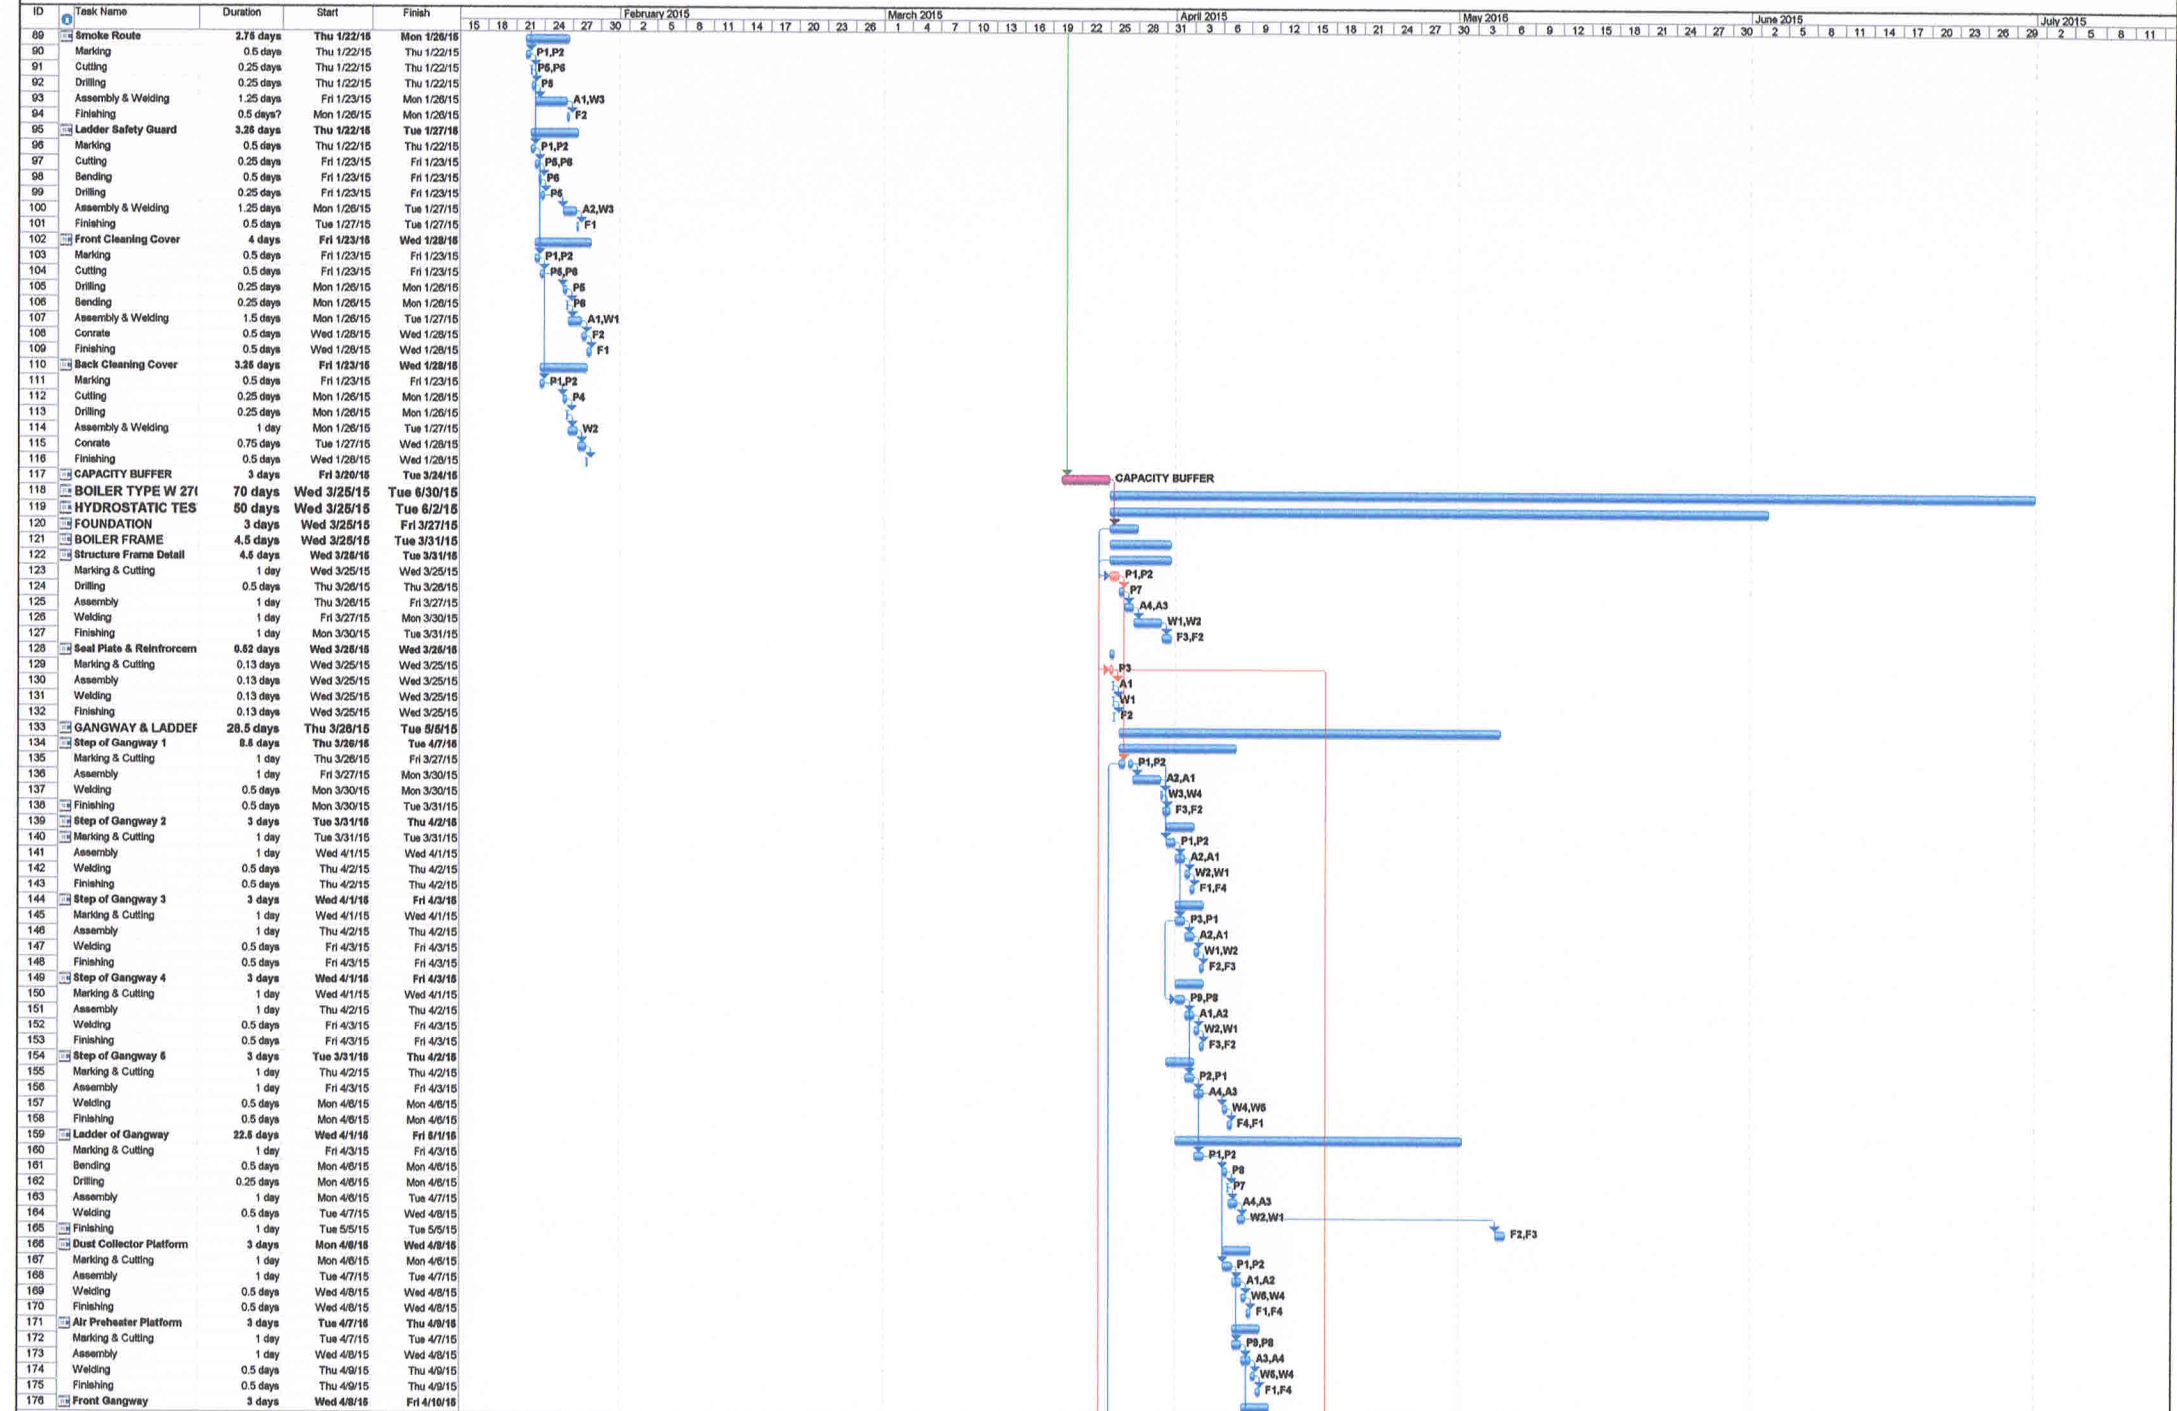

Project: Fire Tube F-80 L den Water T

Legend:


- Task: Progress (Blue bar), Summary (Grey bar), Rolled Up Critical Task (Thick blue bar), Rolled Up Progress (Thick red bar), External Tasks (Thin grey bar), Group By Summary (Thin blue bar)
- Critical Task: Milestone (Red diamond)
- Rolled Up Task: (Thick blue bar)
- Rolled Up Milestone: (Thick blue diamond)
- Split: (Thin red bar)
- Project Summary: (Thin grey bar)
- Deadline: (Thin blue bar)

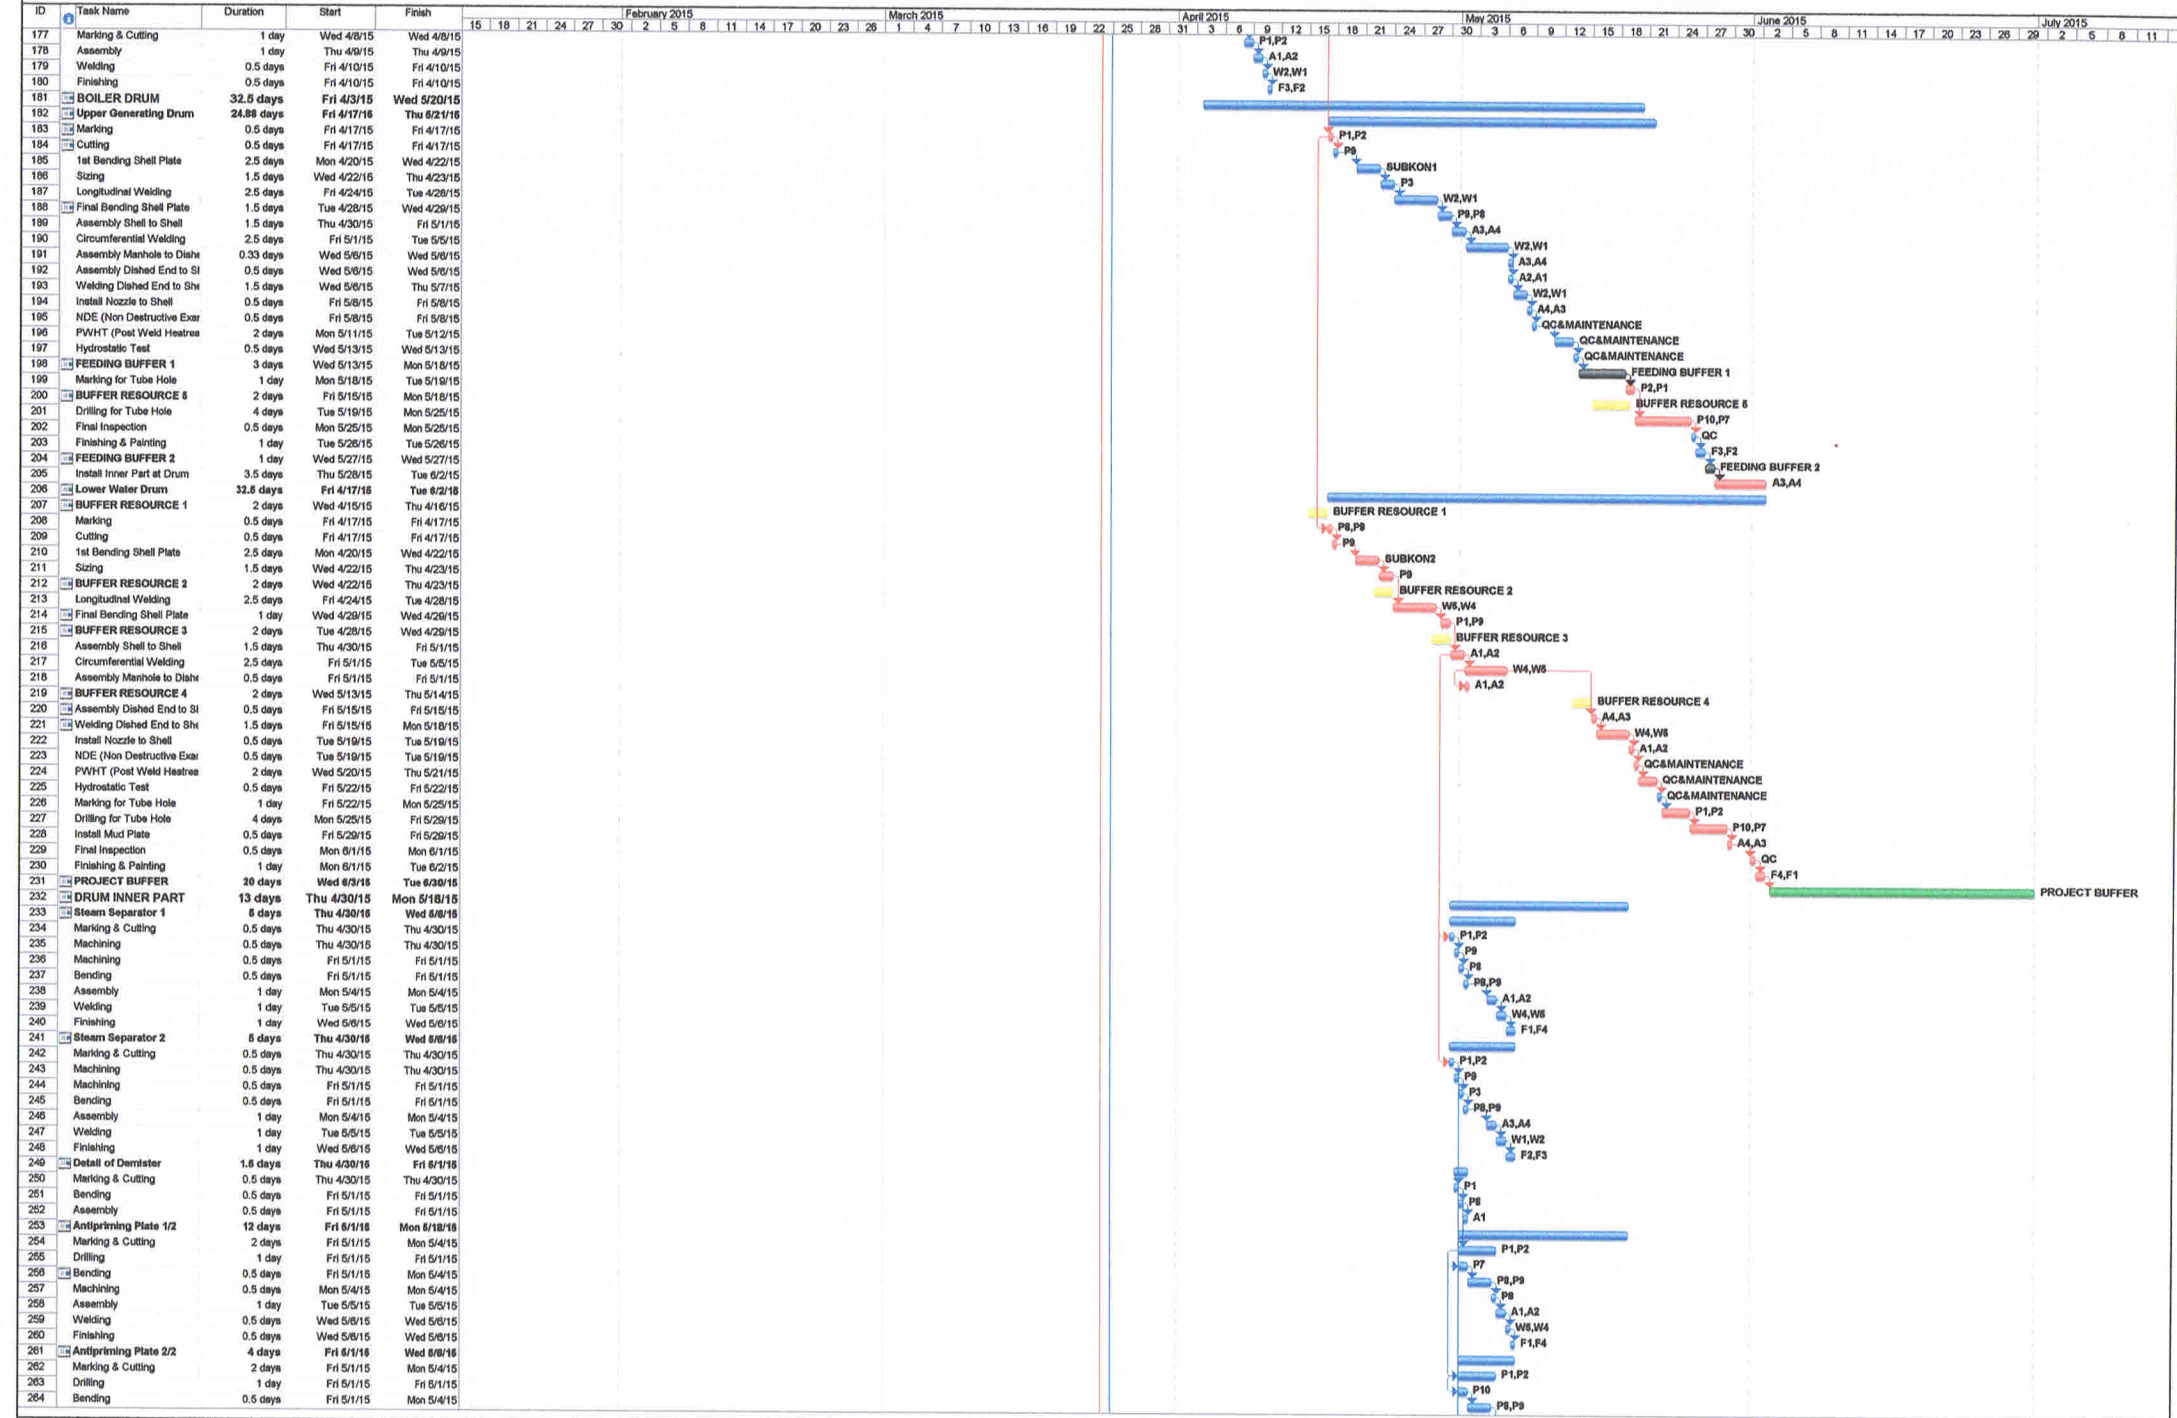


Project: Fire Tube F-80 Lan dan Water T

Legend:

- Progress: Blue bar
- Milestone: Red diamond
- Summary: Grey bar
- Roller Up Critical Task: Blue arrow
- Roller Up Progress: Red arrow
- External Tasks: Green bar
- Group By Summary: Blue arrow
- Roller Up Task: Blue bar
- Roller Up Milestone: Red diamond
- Split: Red diamond
- Project Summary: Blue bar
- Deadline: Blue bar with diamond

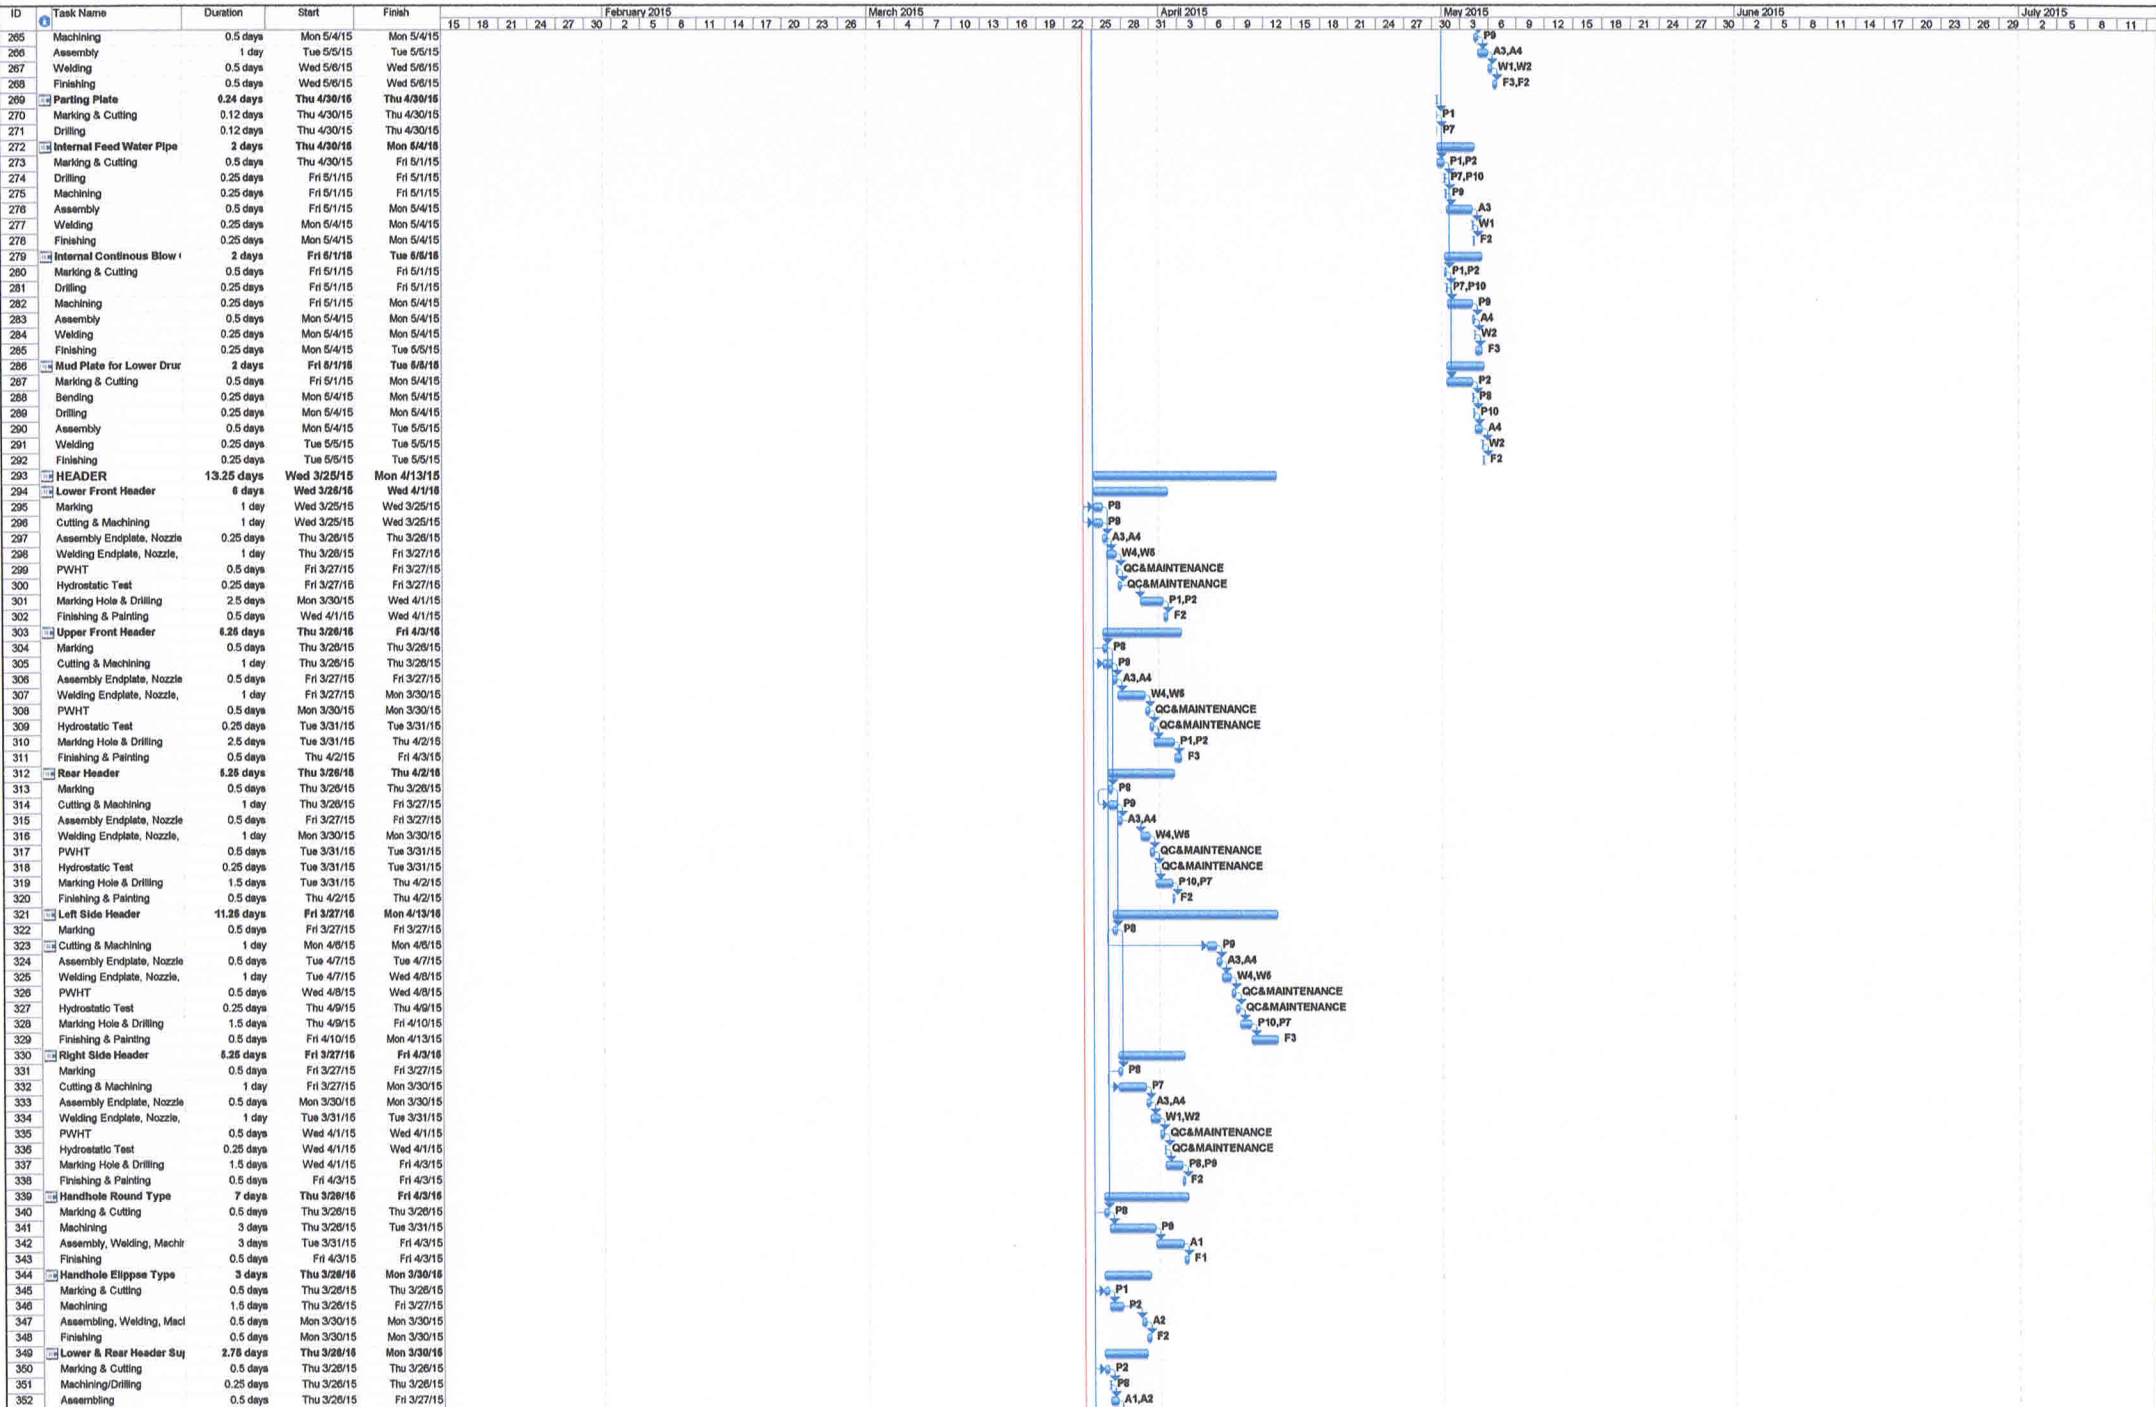

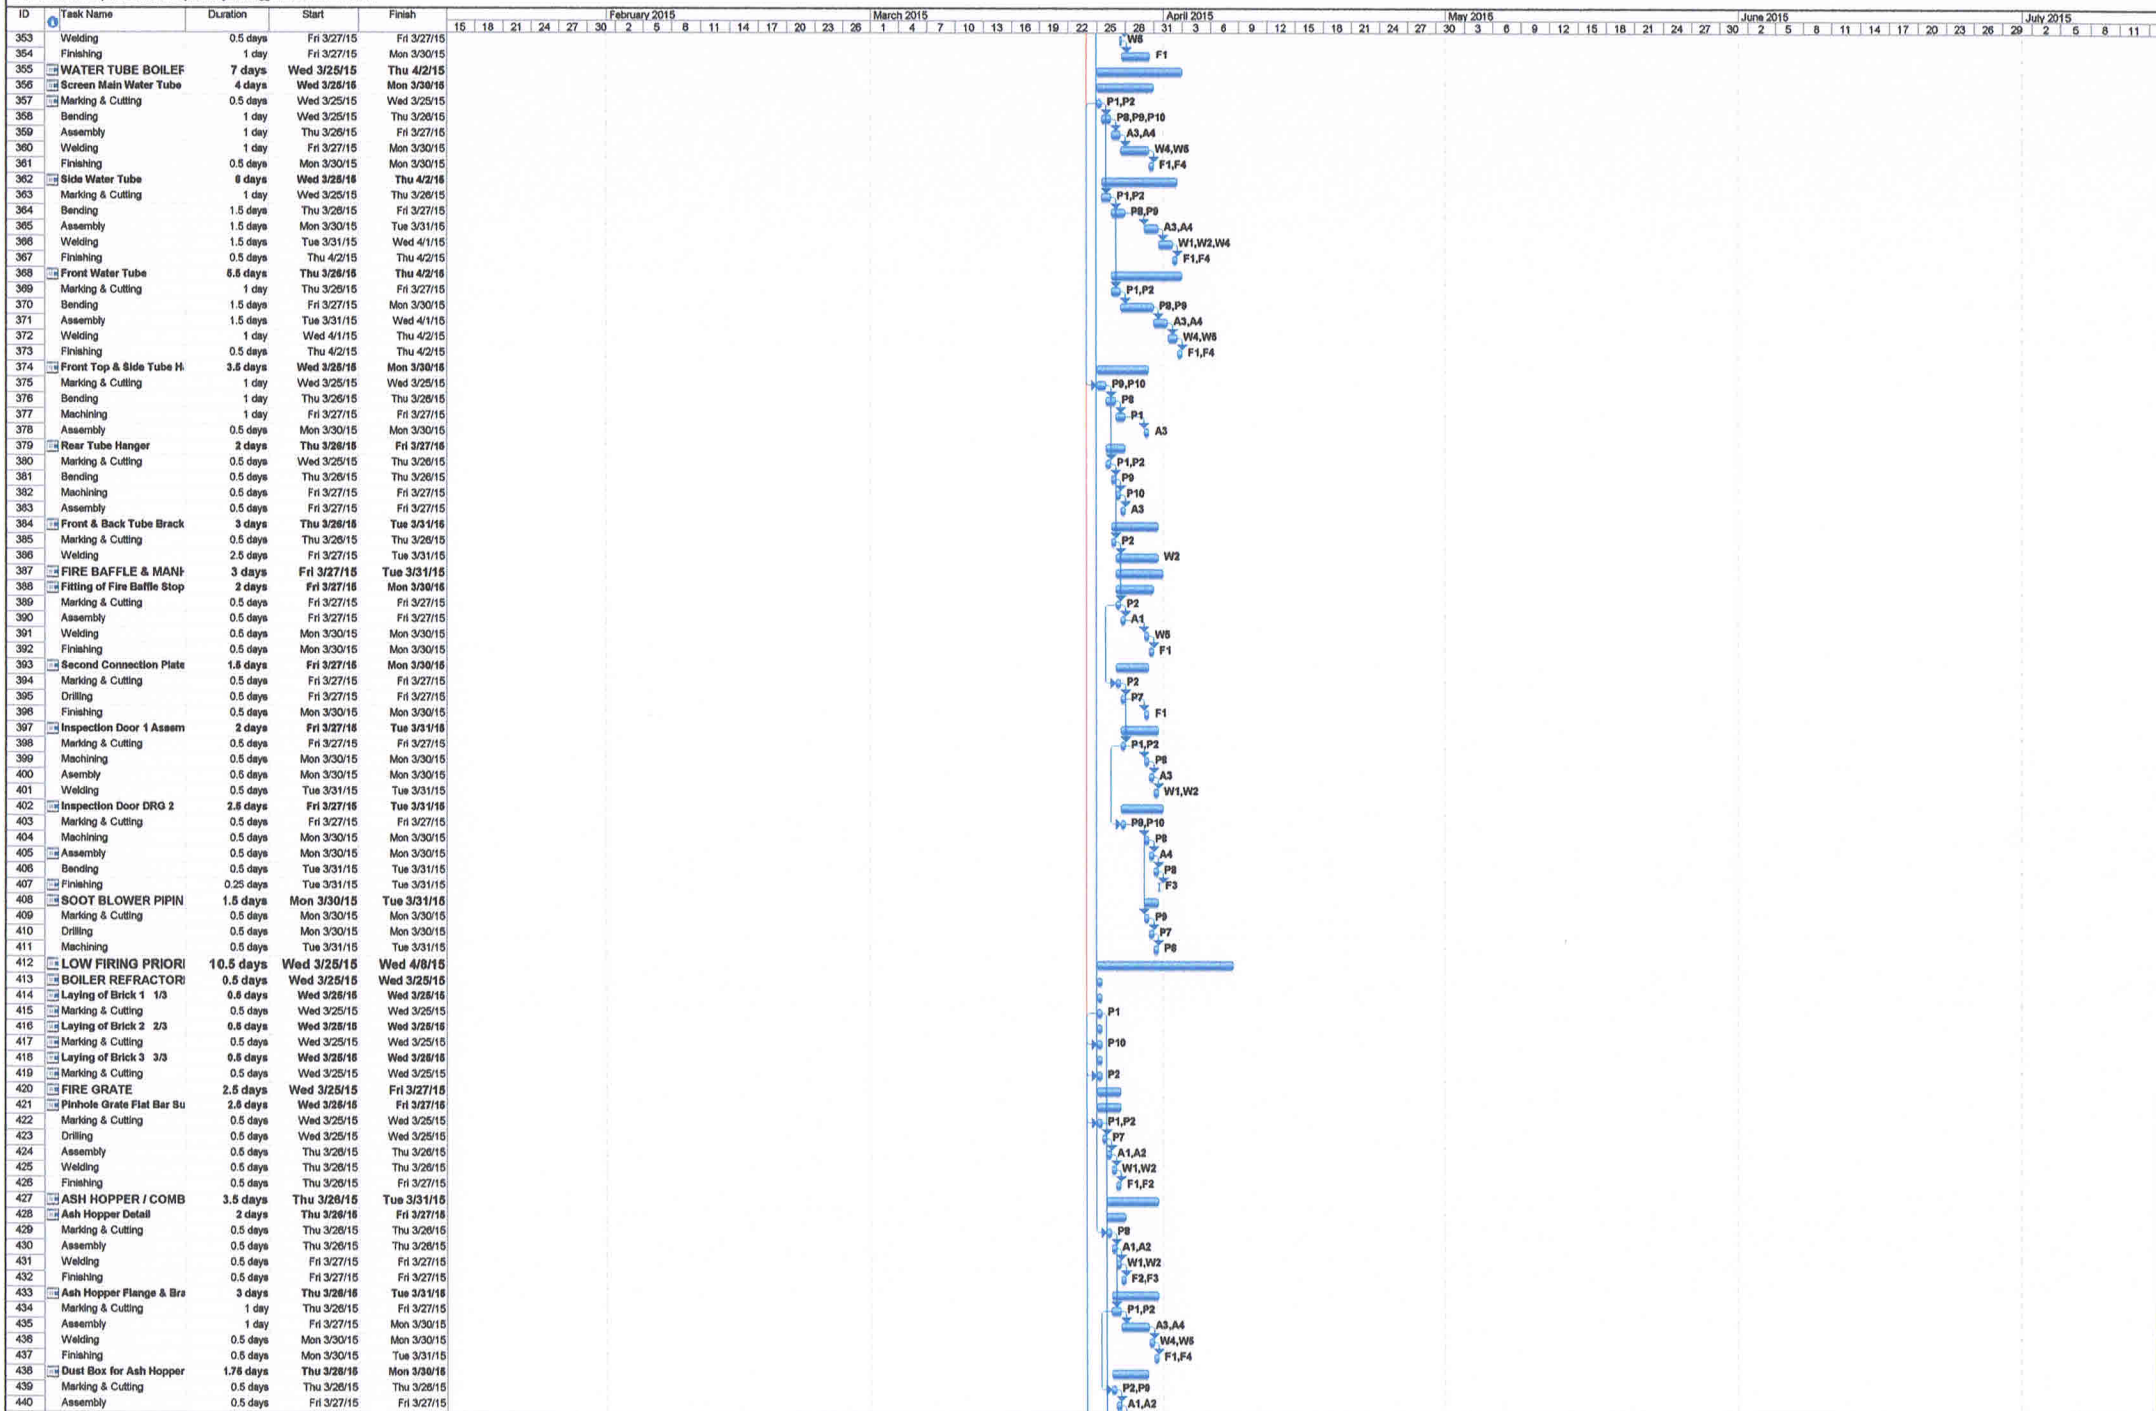

Project: Fire Tube F-80 L dan Water T

Task: Progress Summary Rolled Up Critical Task Rolled Up Progress External Tasks Group By Summary

Critical Task: Milestone Rolled Up Task Rolled Up Milestone Split Project Summary Deadline

Page 5

ID	Task Name	Duration	Start	Finish
441	Drilling	0.25 days	Fri 3/27/15	Fri 3/27/15
442	Finishing	0.5 days	Fri 3/27/15	Mon 3/30/15
443	Screen Break Bearer	1.8 days	Fri 3/27/15	Mon 3/30/15
444	Marking & Cutting	0.5 days	Thu 3/26/15	Fri 3/27/15
445	Bending	0.5 days	Fri 3/27/15	Fri 3/27/15
446	Finishing	0.5 days	Mon 3/30/15	Mon 3/30/15
447	COMBUSTION EQUIP	4 days	Wed 3/25/15	Mon 3/30/15
448	Pendulum Detail (Body)	2 days	Wed 3/25/15	Fri 3/27/15
449	Marking & Cutting	0.5 days	Wed 3/25/15	Wed 3/25/15
450	Drilling	0.5 days	Thu 3/26/15	Thu 3/26/15
451	Bending	0.5 days	Thu 3/26/15	Thu 3/26/15
452	Assembly	0.5 days	Fri 3/27/15	Fri 3/27/15
453	Pendulum Detail (Inner P	3 days	Thu 3/26/15	Mon 3/30/15
454	Marking & Cutting	0.5 days	Wed 3/25/15	Thu 3/26/15
455	Bending	0.5 days	Thu 3/26/15	Thu 3/26/15
456	Assembly	0.5 days	Thu 3/26/15	Fri 3/27/15
457	Machining	0.5 days	Fri 3/27/15	Fri 3/27/15
458	Welding	0.5 days	Mon 3/30/15	Mon 3/30/15
459	Finishing	0.5 days	Mon 3/30/15	Mon 3/30/15
460	Pulsator Detail	2.6 days	Wed 3/25/15	Fri 3/27/15
461	Marking & Cutting	0.5 days	Wed 3/25/15	Wed 3/25/15
462	Drilling	0.5 days	Wed 3/25/15	Wed 3/25/15
463	Assembly	0.5 days	Thu 3/26/15	Thu 3/26/15
464	Welding	0.5 days	Thu 3/26/15	Thu 3/26/15
465	Finishing	0.5 days	Fri 3/27/15	Fri 3/27/15
466	DUST COLLECTOR	7 days	Wed 3/25/15	Thu 4/2/15
467	Dust Collector Frame	6.6 days	Wed 3/25/15	Wed 4/1/15
468	Marking & Cutting	1 day	Wed 3/25/15	Wed 3/25/15
469	Drilling	0.5 days	Thu 3/26/15	Thu 3/26/15
470	Assembly	1 day	Thu 3/26/15	Fri 3/27/15
471	Welding	1 day	Fri 3/27/15	Mon 3/30/15
472	Finishing	1 day	Mon 3/30/15	Tue 3/31/15
473	Rotary Valve Detail	8 days	Thu 3/26/15	Thu 4/2/15
474	Marking & Cutting	1 day	Thu 3/26/15	Thu 3/26/15
475	Machining	1 day	Fri 3/27/15	Fri 3/27/15
476	Drilling	0.5 days	Fri 3/27/15	Mon 3/30/15
477	Assembly	1 day	Mon 3/30/15	Tue 3/31/15
478	Welding	0.5 days	Tue 3/31/15	Tue 3/31/15
479	Finishing	0.5 days	Wed 4/1/15	Wed 4/1/15
480	Dust Box For Dust Collec	3 days	Fri 3/27/15	Tue 3/31/15
481	Marking & Cutting	0.5 days	Fri 3/27/15	Fri 3/27/15
482	Assembly	0.5 days	Fri 3/27/15	Fri 3/27/15
483	Welding	0.5 days	Mon 3/30/15	Mon 3/30/15
484	Finishing	0.5 days	Mon 3/30/15	Mon 3/30/15
485	GAS DUCT	3.6 days	Fri 3/27/15	Wed 4/1/15
486	Gas Duct Detail	3 days	Fri 3/27/15	Wed 4/1/15
487	Marking & Cutting	1 day	Fri 3/27/15	Mon 3/30/15
488	Assembly	0.5 days	Mon 3/30/15	Mon 3/30/15
489	Welding	0.5 days	Tue 3/31/15	Tue 3/31/15
490	Drilling	0.5 days	Tue 3/31/15	Tue 3/31/15
491	Finishing	0.5 days	Wed 4/1/15	Wed 4/1/15
492	Gas Dumper	2.6 days	Mon 3/30/15	Wed 4/1/15
493	Marking & Cutting	0.5 days	Mon 3/30/15	Mon 3/30/15
494	Machining	0.5 days	Tue 3/31/15	Tue 3/31/15
495	Assembly	0.5 days	Tue 3/31/15	Tue 3/31/15
496	Welding	0.5 days	Wed 4/1/15	Wed 4/1/15
497	Finishing	0.5 days	Wed 4/1/15	Wed 4/1/15
498	AIR DUCT	5.5 days	Fri 3/27/15	Fri 4/3/15
499	Bypass Air Duct Detail	3 days	Fri 3/27/15	Wed 4/1/15
500	Marking & Cutting	1 day	Fri 3/27/15	Mon 3/30/15
501	Machining	0.5 days	Mon 3/30/15	Mon 3/30/15
502	Assembly	0.5 days	Tue 3/31/15	Tue 3/31/15
503	Welding	0.5 days	Tue 3/31/15	Tue 3/31/15
504	Finishing	0.5 days	Wed 4/1/15	Wed 4/1/15
505	Primary Air Damper Asse	3.6 days	Mon 3/30/15	Thu 4/2/15
506	Marking & Cutting	1 day	Mon 3/30/15	Tue 3/31/15
507	Bending	0.5 days	Tue 3/31/15	Tue 3/31/15
508	Drilling	0.5 days	Wed 4/1/15	Wed 4/1/15
509	Assembly	0.5 days	Wed 4/1/15	Wed 4/1/15
510	Welding	0.5 days	Wed 4/1/15	Thu 4/2/15
511	Finishing	0.5 days	Thu 4/2/15	Thu 4/2/15
512	Bypass Air Damper Asse	3 days	Mon 3/30/15	Thu 4/2/15
513	Marking & Cutting	1 day	Mon 3/30/15	Tue 3/31/15
514	Machining	0.5 days	Tue 3/31/15	Tue 3/31/15
515	Assembly	0.5 days	Wed 4/1/15	Wed 4/1/15
516	Welding	0.5 days	Thu 4/2/15	Wed 4/1/15
517	Finishing	0.5 days	Thu 4/2/15	Thu 4/2/15
518	Secondary Air Duct Asse	3.8 days	Tue 3/31/15	Fri 4/3/15
519	Marking & Cutting	1 day	Tue 3/31/15	Wed 4/1/15
520	Drilling	0.5 days	Wed 4/1/15	Wed 4/1/15
521	Assembly	1 day	Thu 4/2/15	Thu 4/2/15
522	Welding	0.5 days	Thu 4/2/15	Fri 4/3/15
523	Finishing	0.5 days	Fri 4/3/15	Fri 4/3/15
524	Secondary Air Damper	1.8 days	Tue 3/31/15	Wed 4/1/15
525	Marking & Cutting	0.5 days	Tue 3/31/15	Tue 3/31/15
526	Machining	0.25 days	Wed 4/1/15	Wed 4/1/15
527	Assembly	0.25 days	Wed 4/1/15	Wed 4/1/15
528	Welding	0.25 days	Wed 4/1/15	Wed 4/1/15

